

# Agentic SDLC Software Factory - User Guide

Governed software delivery with Microsoft Foundry and Microsoft Agent Framework

## Contents

---

1. Guide scope
2. Architecture and operating model
3. Roles and access
4. Sign in
  5. Request access
6. Dashboard
7. Create a project
  8. Default Settings
  9. Custom - Step 1: Project details
  10. Custom - Step 2: Requirements and supporting documents
  11. Custom - Step 3: DevOps and repository
  12. Custom - Step 4: Systems of Record
  13. Custom - Step 5: Lifecycle agents and models
  14. Custom - Step 6: Confirm and submit
15. Create a project set
  16. Default Settings
  17. Custom - Step 1: Shared defaults and intake source
  18. Custom - Step 2: Project intake
  19. Custom - Step 3: Shared and per-project agent policy
  20. Custom - Step 4: Confirm and launch
21. Project directories
  22. Existing Projects
  23. Deleted Projects
24. The 12-agent lifecycle
25. Approval gates
26. Workflow execution policies
  27. Human Review
  28. Minimal
  29. Autonomous
30. Project Details workspace
  31. Provisioned systems
  32. Lifecycle
  33. Approval gates
  34. Systems of Record
  35. Generated assets
  36. Agent runs and artifacts
37. Operational screens
  38. Workflow Runs
  39. Human Approval Queue
  40. Agent Activity
  41. Audit Trail
42. Email notifications
43. Generated Azure DevOps assets
  44. Backlog and work-item hierarchy
  45. Sprints
  46. Shared queries
  47. Dashboards
  48. Delivery plan
  49. Test plan and automated run
  50. Project wiki
  51. Azure Repos
52. Generated GitHub assets
  53. Repository
  54. README
  55. Pull request
  56. GitHub Actions deployment
57. Published Azure applications
  58. Published UI
  59. Published API
  60. App Service resources
61. Administration
  62. User Management
  63. Project Access - grant
  64. Project Access - remove
  65. Role Permissions
  66. Agent Configuration
  67. Global Settings
  68. APIM and Configuration
69. In-app documentation
  70. Overview
  71. Architecture
  72. Human-in-the-loop
  73. Agent responsibilities
  74. Security and guardrails

75. [End-to-end operating flow](#)

76. [Screen index](#)

77. [Troubleshooting](#)

78. [Production references](#)

Production edition: August 2026

This guide explains every user-facing screen in the Agentic SDLC Software Factory, the end-to-end Microsoft Agent Framework workflow, the three execution policies, and the generated assets published to Azure DevOps, GitHub, and Azure App Service.

Production application: <https://agentic-sdlc-ui-my.azurewebsites.net>

API health: <https://agentic-sdlc-api-my.azurewebsites.net/api/health>

Screenshots were captured from the deployed production application after release `ff74a1c`. GitHub and published-application images are native browser captures. Azure DevOps and Azure resource images labeled **Live generated evidence** were rendered from live REST responses because unattended browser access stopped at interactive Microsoft sign-in. No synthetic work-item, test, dashboard, wiki, repository, or resource counts are used in those evidence views.

## Guide scope

---


The guide covers:

- Authentication, guest access, access requests, and navigation.
- New Project Default Settings and every step of the Custom workflow.
- New Project Set Default Settings and every step of the Custom workflow.
- Existing and deleted projects, project details, revision, and cleanup evidence.
- Human Review, Minimal, and Autonomous execution policies.
- All 12 ordered Microsoft Foundry Prompt Agents and all nine approval gates.
- Workflow Runs, Human Approval Queue, Agent Activity, and Audit Trail.
- User, project access, role, agent, model, system-of-record, APIM, and configuration administration.
- Generated ADO work items, sprints, queries, dashboards, delivery plan, test plan, test run, wiki, and Azure Repo.
- Generated GitHub repository, README, pull request, and deployment workflow.
- Published Azure UI/API applications and App Service resources.
- Every in-app documentation topic.


## Architecture and operating model

---

The Software Factory separates people, experience, orchestration, model execution, persistence, and systems of record. The Angular/Ionic UI calls a FastAPI service. Microsoft Agent Framework owns the workflow graph, durable pause/resume, and agent sequencing. Every model call crosses Azure API Management before reaching the named Prompt Agent in Microsoft Foundry. Cosmos DB stores production workflow, approval, artifact, audit, project, user, notification, and checkpoint state.

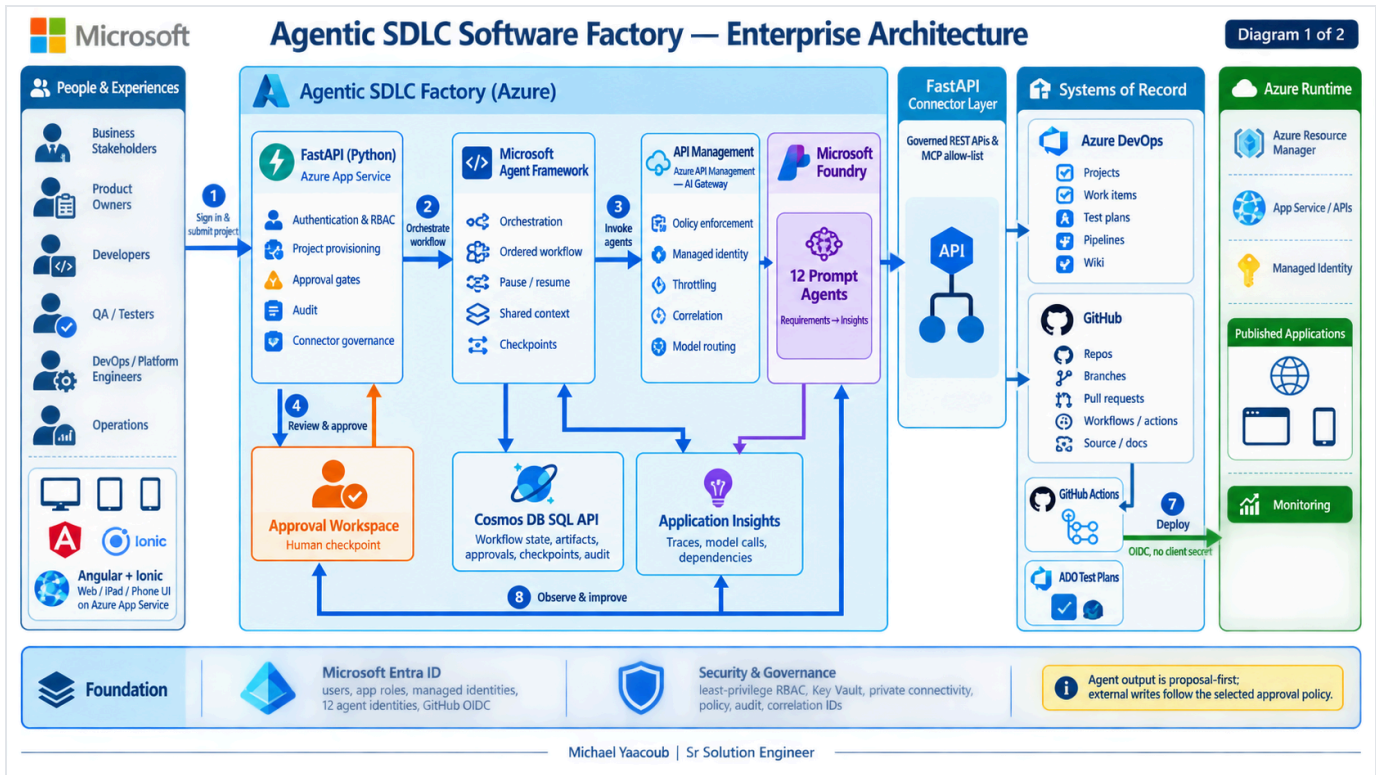

The workflow is deterministic. Agents create proposals and evidence; they do not silently publish external changes. Approval policy and server-side evidence checks decide when reviewed output can update ADO, GitHub, or Azure.

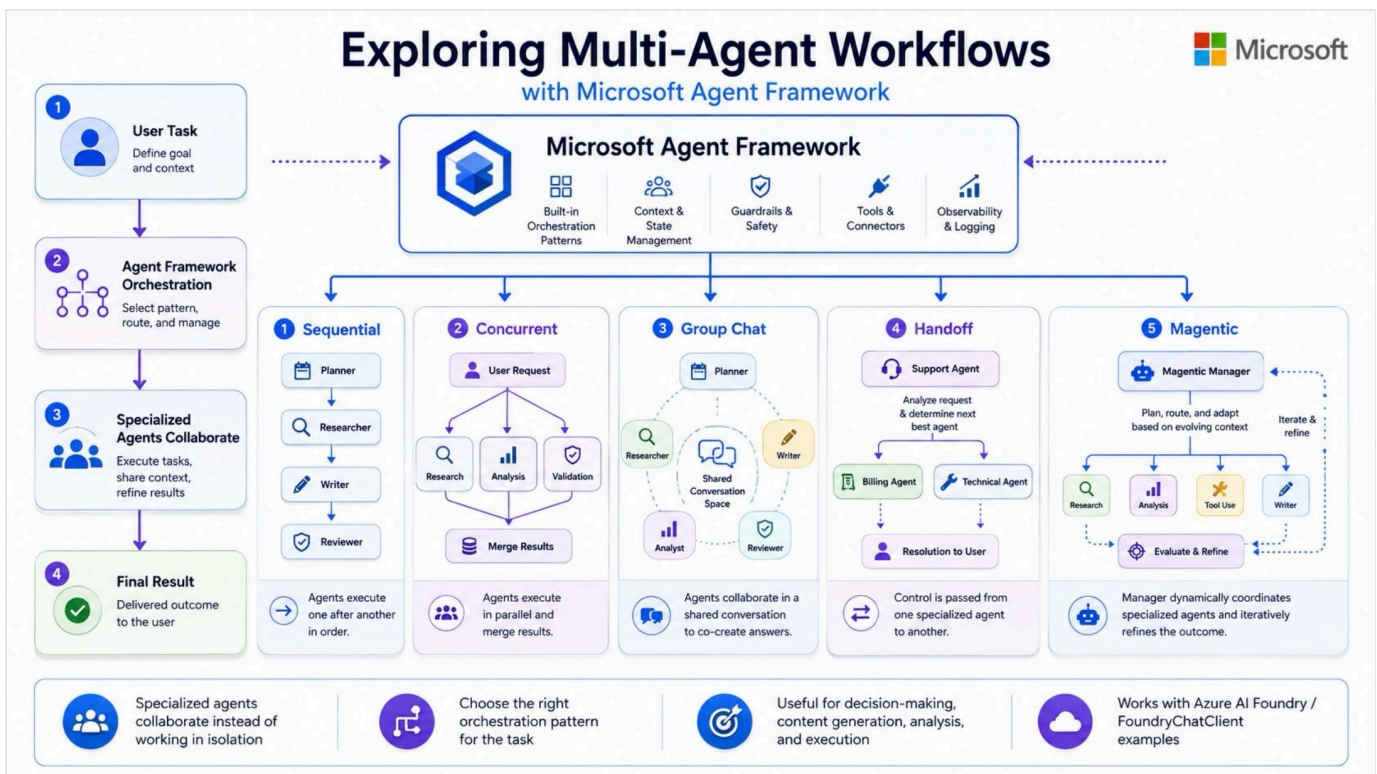



## Roles and access

| Role          | Primary responsibilities                                                                           |
|---------------|----------------------------------------------------------------------------------------------------|
| App Owner     | Full application administration, project access, permissions, configuration, audit, and deletion.  |
| Admin         | Agent, project, test, security, and operational administration according to the permission matrix. |
| IT User       | Architecture, implementation, pull-request, release, platform, and operational decisions.          |
| Business User | Scope, requirements, backlog, outcomes, and improvement decisions.                                 |
| Guest         | Read-only exploration of allowed application content.                                              |

The API is authoritative. Hiding a button in the UI does not grant or remove permission; each operation is checked again against the effective capability matrix.

## Sign in

The sign-in screen supports three paths:

- Internal users on the configured tenant use Microsoft Entra ID single sign-on.
- External users use an email one-time passcode.
- Guests can continue with read-only access.

Enter an email address and select **Sign in with your email**. External users enter the six-digit code delivered by Azure Communication Services. Internal tenant users can choose **Sign in with Microsoft Entra ID**. The signed-in identity, provider, role, and effective capabilities determine visible navigation and API authorization.



# Agentic SDLC — Software Factory

Orchestrate Azure AI Foundry agents across the software lifecycle — with governance from stage-by-stage review to autonomous execution.



## Agentic SDLC

Foundry agents plan, design, build, test, and operate — you stay in control.



## Governed access

Entra ID for staff, one-time codes for partners, guest read-only for everyone else.



## Configurable governance

Choose human review at every stage, minimal checkpoints, or fully autonomous execution.

Powered by Azure AI Foundry & Azure API Management  
Michael Yaacoub | Sr Solution Engineer — [LinkedIn](#) · [GitHub](#)

## Sign in

Enter your email address and we'll send you a one-time passcode. Accounts on **MngEnvMCAP829495.onmicrosoft.com** use Microsoft Entra ID single sign-on instead. Or continue as a guest for read-only access.

### Email address

✉ you@company.com

Quick fill: • @MngEnvMCAP829495.onmicrosoft.com

• @microsoft.com

✉ Sign in with your email

On MngEnvMCAP829495.onmicrosoft.com?

[Sign in with Microsoft Entra ID](#)

OR

👤 Continue as guest (read-only)

Guests can explore generated artifacts and reference data. They cannot create, edit, approve, or deploy.

Don't have an account?

[Request access](#)

## Request access

A person without an account can open **Request access**, enter identity and business context, and submit the request for App Owner review. The form itself does not grant permissions.



# Agentic SDLC — Software Factory

Orchestrate Azure AI Foundry agents across the software lifecycle — with governance from stage-by-stage review to autonomous execution.



## Agentic SDLC

Foundry agents plan, design, build, test, and operate — you stay in control.



## Governed access

Entra ID for staff, one-time codes for partners, guest read-only for everyone else.



## Configurable governance

Choose human review at every stage, minimal checkpoints, or fully autonomous execution.

Powered by Azure AI Foundry & Azure API Management  
Michael Yaacoub | Sr Solution Engineer — [LinkedIn](#) · [GitHub](#)

## Sign in

Enter your email address and we'll send you a one-time passcode. Accounts on **MngEnvMCAP829495.onmicrosoft.com** use Microsoft Entra ID single sign-on instead. Or continue as a guest for read-only access.

### Email address

you@company.com

Quick fill: • @MngEnvMCAP829495.onmicrosoft.com

• @microsoft.com

Sign in with your email

On MngEnvMCAP829495.onmicrosoft.com?

[Sign in with Microsoft Entra ID](#)

OR

Continue as guest (read-only)

Guests can explore generated artifacts and reference data. They cannot create, edit, approve, or deploy.

Don't have an account?

[Request access](#)

## Dashboard

The dashboard is the operational landing page. It summarizes project counts, pending approvals, active workflow state, and recent projects. Use it to decide whether to review a gate, inspect a running project, or create new work.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Welcome, Michael

Agentic SDLC operations at a glance.

ACTIVE PROJECTS

4

4 total, including archived

WORKFLOW RUNS

4

0 currently running

PENDING APPROVALS

3

Gates awaiting a decision

Recent projects

The six most recently created projects.

PROJECT

STAGE

ENVIRONMENT

BUSINESS OWNER

STATUS

Fleet Inspection And Maintenance

No description

Deploy

Dev

myaacoub@microsoft.com

Awaiting Approval

Field service Work Orders

No description

Deploy

Dev

myaacoub@microsoft.com

Awaiting Approval

Equipment Calibration Compliance

No description

Improve

Dev

myaacoub@microsoft.com

Approved

Construction Site Progress Capture

No description

Improve

Dev

myaacoub@microsoft.com

Approved

## Create a project

New Project opens on **Default Settings**. This is the recommended path for most work because global connector, model, lifecycle-agent, environment, and system-of-record settings already define a governed baseline.

### Default Settings

Default Settings asks only for:

- Project name.
- Optional description.
- Owner. The same value is saved as both Business Owner and IT Owner.
- Workflow execution policy: Human Review, Minimal, or Autonomous.
- Requirements text or an attached readable requirements document.
- Optional supporting documents attached with the paperclip action.

If requirements are typed, the client creates a Markdown requirements document. If text is blank, the first readable attachment becomes the requirements source. Remaining uploads are supporting evidence. No template download is required.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

New Project

Start with the essentials or switch to Custom for full delivery controls.

DEFAULT SETTINGS

CUSTOM

FAST SETUP

Project essentials

Factory defaults handle environments, systems of record, repositories, and lifecycle agents.

Default policy

Details

Project name \*  
Customer Onboarding Portal

Description  
A concise description of the product and outcome.

Owner \*  
owner@company.com

Workflow execution  
Human Review

Pause at every approval gate. Approval automatically starts the next eligible Foundry agents.

PROJECT BRIEF

Requirements

Required

Requirements  
Describe the users, goals, workflows, constraints, and expected outcomes.

Attach files

Requirements or supporting documents - 25 MB each

0 attached documents

Create & start workflow

Select **Create & start workflow** only after name, owner, and requirements are present. The API provisions project systems, publishes intake documents, creates the durable workflow run, and starts eligible agents according to policy.

## Custom - Step 1: Project details

Custom exposes every project-level control. Step 1 separates Business Owner and IT Owner and lets the creator choose workflow execution explicitly.



Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

New Project

Start with the essentials or switch to Custom for full delivery controls.

DEFAULT SETTINGS

CUSTOM

Step 1 of 6

Project details

Project details

Who owns this work and what is it called.

Project details

Project name \*

Customer Service Modernization

Description

Modernize customer service intake, routing, and operational reporting.

Business owner \*

business.owner@contoso.com

IT owner

it.owner@contoso.com

Workflow execution

Human Review

Pause at every approval gate. Approval automatically starts the next eligible Foundry agents.

Back

Continue

## Custom - Step 2: Requirements and supporting documents

Type requirements directly or attach a readable requirements file. Add architecture notes, technical constraints, mockups, images, presentations, or other supporting evidence with the same attachment action. Each file is limited to 25 MB.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

New Project

Start with the essentials or switch to Custom for full delivery controls.

DEFAULT SETTINGS

CUSTOM

Step 2 of 6

Requirements & supporting documents

Requirements are required; UX and technical documents are optional.

PROJECT BRIEF

Requirements

Requirements

Customer service agents must capture requests, route work by priority, track service levels, and give supervisors real-time operational visibility.

Attach files

Requirements or supporting documents - 25 MB each

Back

Continue

## Custom - Step 3: DevOps and repository

This step overrides inherited ADO organization/project, GitHub repository, GitHub visibility, and target environment values. ADO visibility is connector-restricted to the organization-supported value.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

New Project

Start with the essentials or switch to Custom for full delivery controls.

DEFAULT SETTINGS

CUSTOM

Step 3 of 6

DevOps & repository

DevOps & repository

Where backlog items, code, and deployments land.

DevOps & repository

Azure DevOps organization

https://dev.azure.com/csdmichael

Azure DevOps project

Defaults to the project name

Azure DevOps project visibility

Private

GitHub repository

csdmichael/

GitHub repository visibility

Public

ⓘ Azure DevOps projects are always private because the organisation does not permit public projects. GitHub repositories can be public or private; in production the recommended default is private.

Target environment

Dev

Back

Continue

## Custom - Step 4: Systems of Record

Global settings are inherited by default. Toggle an override only when this project must use a different provider, URL, project, repository, or path. Untouched rows continue to follow global administration.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

New Project

Start with the essentials or switch to Custom for full delivery controls.

DEFAULT SETTINGS

CUSTOM

Step 4 of 6

Systems of Record

Inherited from global settings; override only what differs.

Systems of Record

Pre-populated from the global settings. Toggle **Override** on any row this project should track somewhere else; untouched rows keep inheriting the global value.

|                          |                                  |                                                                                                            |
|--------------------------|----------------------------------|------------------------------------------------------------------------------------------------------------|
| <input type="checkbox"/> | Documentation                    | Inherited: GitHub docs/ folder · <a href="https://github.com/csdmichael">https://github.com/csdmichael</a> |
| <input type="checkbox"/> | Work Items Tracking              | Inherited: Azure DevOps · <a href="https://dev.azure.com/csdmichael">https://dev.azure.com/csdmichael</a>  |
| <input type="checkbox"/> | Test Cases & Test Plans Tracking | Inherited: Azure DevOps · <a href="https://dev.azure.com/csdmichael">https://dev.azure.com/csdmichael</a>  |
| <input type="checkbox"/> | Code Build / Pipelines           | Inherited: Azure DevOps · <a href="https://dev.azure.com/csdmichael">https://dev.azure.com/csdmichael</a>  |
| <input type="checkbox"/> | Source Code Org                  | Inherited: GitHub · <a href="https://github.com/csdmichael">https://github.com/csdmichael</a>              |

Back

Continue

## Custom - Step 5: Lifecycle agents and models

All enabled agents are selected by default. Clear an agent only when the project intentionally excludes that lifecycle responsibility. Model dropdowns inherit global model policy; a project override applies to future agent runs and revisions.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

New Project

Start with the essentials or switch to Custom for full delivery controls.

DEFAULT SETTINGS

CUSTOM

Step 5 of 6

Lifecycle agents

Lifecycle agents

Which specialized Foundry agents run for this project.

Lifecycle agents

Select which specialized Foundry agents participate. The server runs eligible agents automatically and pauses only where the selected execution policy requires review.

|                                     |                            |                                                          |                                           |
|-------------------------------------|----------------------------|----------------------------------------------------------|-------------------------------------------|
| <input checked="" type="checkbox"/> | Requirements Agent         | plan · inherits global default · approval: business_user | model-router (balanced: cost + quality) ▾ |
| <input checked="" type="checkbox"/> | Planning Agent             | plan · inherits global default · approval: business_user | model-router (balanced: cost + quality) ▾ |
| <input checked="" type="checkbox"/> | Architecture Advisor Agent | design · inherits global default · approval: it_user     | gpt-5.4 ▾                                 |
| <input checked="" type="checkbox"/> | Code Generation Agent      | build · inherits global default · approval: it_user      | gpt-5.1-codex ▾                           |
| <input checked="" type="checkbox"/> | Test Planning Agent        | test · inherits global default · approval: it_user       | model-router (balanced: cost + quality) ▾ |
| <input checked="" type="checkbox"/> | Testing Agent              | test · inherits global default · approval: admin         | gpt-5.1-codex ▾                           |
| <input checked="" type="checkbox"/> | Test Automation Agent      | test · inherits global default · approval: admin         | gpt-5.1-codex ▾                           |

## Custom - Step 6: Confirm and submit

The confirmation screen summarizes ownership, intake, ADO/GitHub targets, environment, policy, system overrides, selected agents, and model overrides. **Create & start workflow** is the only action that provisions resources.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Confirm & submit

|                              |                                |
|------------------------------|--------------------------------|
| Name                         | Customer Service Modernization |
| Business owner               | business.owner@contoso.com     |
| Requirements                 | Typed requirements             |
| Supporting documents         | 0                              |
| ADO                          | Customer Service Modernization |
| ADO visibility               | private                        |
| GitHub                       | csdmichael/                    |
| GitHub visibility            | public                         |
| Environment                  | Dev                            |
| Workflow execution           | Human Review                   |
| Systems of Record overridden | None (all inherited)           |
| Agents selected              | 12                             |
| Agent model overrides        | 0                              |

Pause at every approval gate. Approval automatically starts the next eligible Foundry agents.

Back

Create & start workflow

## Create a project set

Project sets create two to twenty independent projects with separate workflow runs, approvals, checkpoints, artifacts, and audit records. Runs advance concurrently with a bounded worker pool.

### Default Settings

The streamlined set builder applies one owner and one execution policy to every project. Each project brief contains its own name, description, requirements text, and supporting attachments. Add or remove briefs before launch; at least two valid projects are required.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

New Project Set

Create several independent projects with shared defaults, or customize the full launch policy.

DEFAULT SETTINGS

CUSTOM

PORTFOLIO SETUP

Shared defaults

Owner and workflow policy apply to every project in this set.

Project set name \*  
Customer experience modernization

Owner \*  
owner@company.com

Workflow execution  
Autonomous

1 Project brief

Project name \*  
Returns portal

Description  
What this project delivers.

Requirements  
Describe users, workflows, constraints, and expected outcomes.

Attach files

Requirements or supporting documents - 25 MB each

2 Project brief

Project name \*  
Returns portal

Description

Requirements  
Describe users, workflows, constraints, and expected outcomes.

## Custom - Step 1: Shared defaults and intake source

Custom separates default Business/IT owners and environment. Choose the manual wizard or a validated folder-per-project ZIP. ZIP intake requires one functional requirements document per top-level project folder; technical and UX files are optional.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

New Project Set

Create several independent projects with shared defaults, or customize the full launch policy.

DEFAULT SETTINGS

CUSTOM

Step 1 of 4

Set defaults

Project set name \*

Customer Operations Portfolio

Default business owner \*

business.owner@contoso.com

Default IT owner

it.owner@contoso.com

Default environment

Dev

Intake source

WIZARD

ZIP IMPORT

Workflow

Models

Execution

Autonomous by default

Shared across the set

Parallel per project

Back

Continue

2 projects

## Custom - Step 2: Project intake

For manual intake, each project can override its name, description, owners, and execution policy and use the same typed-or-attached requirements composer as New Project. The ZIP path previews folders and classified documents before creation.



Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

New Project Set

Create several independent projects with shared defaults, or customize the full launch policy.

DEFAULT SETTINGS

CUSTOM

Step 2 of 4

Project intake

Project intake

2 projects

1 Project

Name \*

Customer Intake Portal

Description

Business owner

business.owner@contoso.com

IT owner

it.owner@contoso.com

Workflow execution

Autonomous

Requirements

Agents capture, classify, and route customer requests with service-level tracking.

2 Project

Name \*

Service Operations Dashboard

Description

Business owner

business.owner@contoso.com

IT owner

it.owner@contoso.com

Workflow execution

Autonomous

Requirements

Supervisors monitor queues, escalations, throughput, and service-level performance.

## Custom - Step 3: Shared and per-project agent policy

Shared agent/model configuration applies across the set. A project can replace that policy without changing sibling projects. This enables one portfolio to compare models or exclude an agent for a specific project.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Step 3 of 4

Agent configuration

2 projects

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Agent configuration

0 model overrides

Shared configuration

Applied to every project unless overridden.

|                                     |                                        |                         |
|-------------------------------------|----------------------------------------|-------------------------|
| <input checked="" type="checkbox"/> | Requirements Agent plan                | model-router (balanced) |
| <input checked="" type="checkbox"/> | Planning Agent plan                    | model-router (balanced) |
| <input checked="" type="checkbox"/> | Architecture Advisor Agent design      | gpt-5.4                 |
| <input checked="" type="checkbox"/> | Code Generation Agent build            | gpt-5.1-codex           |
| <input checked="" type="checkbox"/> | Test Planning Agent test               | model-router (balanced) |
| <input checked="" type="checkbox"/> | Testing Agent test                     | gpt-5.1-codex           |
| <input checked="" type="checkbox"/> | Test Automation Agent test             | gpt-5.1-codex           |
| <input checked="" type="checkbox"/> | Security and Compliance Agent security | gpt-5.4                 |
| <input checked="" type="checkbox"/> | DevOps / Release Agent deploy          | gpt-5.4                 |
| <input checked="" type="checkbox"/> | Ops Monitoring Agent operate           | model-router (balanced) |
| <input checked="" type="checkbox"/> | Knowledge Assistant operate            | model-router (balanced) |
| <input checked="" type="checkbox"/> | Insights Agent improve                 | model-router (balanced) |

Back

Project overrides

Keep shared settings or replace them for one project.

Customer Intake Portal

Shared configuration

Override

Service Operations Dashboard

Shared configuration

Override

Continue

## Custom - Step 4: Confirm and launch

Review project count, shared agents, model overrides, project execution policies, and launch mode. Each project receives its own durable run even though the set is submitted once.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

New Project Set

Create several independent projects with shared defaults, or customize the full launch policy.

DEFAULT SETTINGS

CUSTOM

Step 4 of 4

Confirm & launch

2 Projects

12 Shared agents

0 Shared model overrides

Parallel Workflow launch

1 Customer Intake Portal

business.owner@contoso.com · Dev

Autonomous

Shared models

2 Service Operations Dashboard

business.owner@contoso.com · Dev

Autonomous

Shared models

Back

Create set & launch

## Project directories

### Existing Projects

Existing Projects groups and filters project cards by project set, state, execution mode, and text. Cards show status-aware progress and open the detailed workflow workspace.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

New project setNew project

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Existing Projects

4 project(s) - 4 shown

Search by name, owner, or description

StatusAll statuses

Project setAll project sets

Complete2

Equipment Calibration Compliance

Enterprise Demo Project Set - Validation

No description

ImproveDevAutonomousMyaacoub@Microsoft.Com

Workflow progress100%

Workflow complete

Trace - ImproveWorkflow complete8/27/26, 10:30 AM

Updated Aug 27, 2026

Construction Site Progress Capture

Enterprise Demo Project Set - Validation

No description

ImproveDevAutonomousMyaacoub@Microsoft.Com

Workflow progress100%

Workflow complete

Trace - ImproveWorkflow complete8/27/26, 4:45 AM

Updated Aug 27, 2026

Awaiting Approval2

Fleet Inspection And Maintenance

Enterprise Demo Project Set - Validation

No description

Field service Work Orders

Enterprise Demo Project Set - Validation

No description

## Deleted Projects

Deleted Projects is a read-only audit projection. It retains who deleted the project, when it was deleted, its last state and execution mode, and the outcome of selected ADO, GitHub, Azure, and local cleanup operations.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Deleted Projects

Permanent deletion records and external cleanup outcomes.

Search deleted projects

28 of 28

| PROJECT                                                                                         | EXECUTION             | LAST WORKFLOW STATE        | DELETED                                                            | EXTERNAL CLEANUP                                                                         |
|-------------------------------------------------------------------------------------------------|-----------------------|----------------------------|--------------------------------------------------------------------|------------------------------------------------------------------------------------------|
| To do list<br>myaacoub@microsoft.com                                                            | Autonomous<br>Dev     | Test<br>AwaitingApproval   | Aug 27, 2026, 8:17:56 PM<br>admin@mngenvmcap829495.onmicrosoft.com | <div>Azure DevOps: retained</div> <div>GitHub: retained</div> <div>Azure: retained</div> |
| Interactive Chip Simulation and Education website<br>Project Set Demo<br>myaacoub@microsoft.com | Autonomous<br>Dev     | Deploy<br>AwaitingApproval | Aug 27, 2026, 8:16:45 PM<br>admin@mngenvmcap829495.onmicrosoft.com | <div>Azure DevOps: deleted</div> <div>GitHub: deleted</div> <div>Azure: retained</div>   |
| Retail Store Task Execution<br>Project Set Demo<br>myaacoub@microsoft.com                       | Minimal review<br>Dev | Plan<br>AwaitingApproval   | Aug 27, 2026, 8:16:26 PM<br>admin@mngenvmcap829495.onmicrosoft.com | <div>Azure DevOps: deleted</div> <div>GitHub: deleted</div> <div>Azure: retained</div>   |
| Returns And Reverse Logistics<br>Project Set Demo<br>myaacoub@microsoft.com                     | Human review<br>Dev   | Plan<br>AwaitingApproval   | Aug 27, 2026, 8:16:16 PM<br>admin@mngenvmcap829495.onmicrosoft.com | <div>Azure DevOps: deleted</div> <div>GitHub: deleted</div> <div>Azure: retained</div>   |
| Player Loyalty<br>Project Set Demo<br>myaacoub@microsoft.com                                    | Autonomous<br>Dev     | Deploy<br>AwaitingApproval | Aug 27, 2026, 8:16:00 PM<br>admin@mngenvmcap829495.onmicrosoft.com | <div>Azure DevOps: deleted</div> <div>GitHub: deleted</div> <div>Azure: retained</div>   |
| To do list<br>myaacoub@microsoft.com                                                            | Autonomous<br>Dev     | Plan<br>Draft              | Aug 27, 2026, 7:58:52 PM<br>admin@mngenvmcap829495.onmicrosoft.com | <div>Azure DevOps: skipped</div> <div>GitHub: skipped</div> <div>Azure: skipped</div>    |
| Construction Site Progress Capture<br>Enterprise Demo Project Set<br>myaacoub@microsoft.com     | Autonomous<br>Dev     | Improve<br>Approved        | Aug 27, 2026, 4:02:24 AM<br>myaacoub@microsoft.com                 | <div>Azure DevOps: deleted</div> <div>GitHub: deleted</div> <div>Azure: deleted</div>    |

# The 12-agent lifecycle

Every project uses the same ordered topology. The selected execution policy changes who approves a gate, not agent responsibilities, evidence requirements, connector boundaries, or audit behavior.

| Order | Agent                         | Stage    | Primary output                                                                      |
|-------|-------------------------------|----------|-------------------------------------------------------------------------------------|
| 010   | Requirements Agent            | Plan     | Scope, actors, functional/non-functional requirements, constraints, risks.          |
| 020   | Planning Agent                | Plan     | Epic, Features, User Stories, Tasks, estimates, priorities, acceptance criteria.    |
| 030   | Architecture Advisor Agent    | Design   | Architecture, data model, API contracts, threat-model and implementation decisions. |
| 040   | Code Generation Agent         | Build    | Application scaffold, database, tests, pipelines, branch, and pull request.         |
| 050   | Test Planning Agent           | Test     | Test strategy, suites, cases, and requirement traceability.                         |
| 060   | Testing Agent                 | Test     | Exact-commit CI assessment, defects, quality evidence, and readiness.               |
| 070   | Test Automation Agent         | Test     | Automated runs, result evidence, and ADO test updates.                              |
| 080   | Security and Compliance Agent | Security | Findings, severity, mitigation, residual risk, promotion recommendation.            |
| 090   | DevOps / Release Agent        | Deploy   | OIDC, Azure hosting, merge, deployment, smoke tests, and release record.            |
| 100   | Ops Monitoring Agent          | Operate  | Health indicators, alerts, dashboards, incidents, and runbooks.                     |
| 110   | Knowledge Assistant           | Operate  | Cited project and operational knowledge brief.                                      |

| Order | Agent          | Stage   | Primary output                                                           |
|-------|----------------|---------|--------------------------------------------------------------------------|
| 120   | Insights Agent | Improve | Metrics, thresholds, trends, risks, and prioritized improvement backlog. |

## Approval gates

Nine gates separate generation from publication:

1. Plan and Scope Approval.
2. Backlog Generation Approval.
3. Architecture and Design Approval.
4. Code Generation Approval.
5. Pull Request Review Approval.
6. Test Acceptance Approval.
7. Security Review Approval.
8. Release and Deployment Approval.
9. Operate and Improve Approval.


A gate cannot publish until its prerequisite is approved and required artifact/tool evidence exists. Approve records the selected artifacts and triggers publication. Request Changes requires a comment and returns the owning agent output for revision. Reject closes the decision. Delegate records the replacement approver. Every transition is appended to the audit trail.

## Workflow execution policies

| Policy       | Human checkpoints        | Behavior                                                                                                        |
|--------------|--------------------------|-----------------------------------------------------------------------------------------------------------------|
| Human Review | All nine gates           | A person reviews every proposal and publication action.                                                         |
| Minimal      | Four consequential gates | Routine evidence gates advance automatically; backlog, architecture, pull request, and release decisions pause. |
| Autonomous   | None                     | Policy validates evidence and records automated decisions across the full lifecycle.                            |

### Human Review

Human Review is intended for regulated, unfamiliar, high-impact, or first-of-kind work.

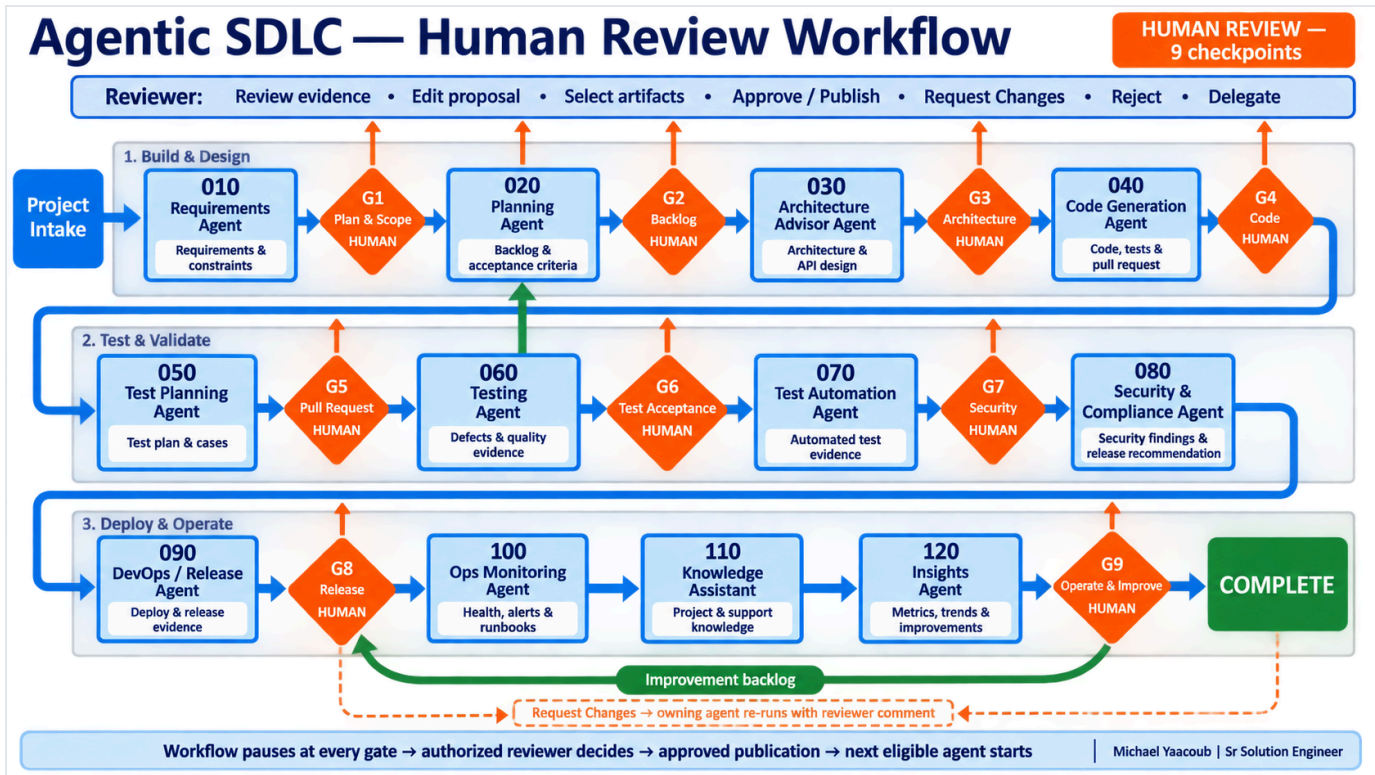

The Fleet Inspection and Maintenance project shows the live full-review state. Overview identifies owners, environment, targets, current stage, and policy.

**Agentic SDLC — Software Factory**

**Agentic SDLC**  
Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

**Fleet Inspection And Maintenance**

No description

Existing projects

AwaitingApproval

Delete project

**Overview**

Intake details captured when the project was created.

|                                  |                        |                                  |                             |               |
|----------------------------------|------------------------|----------------------------------|-----------------------------|---------------|
| BUSINESS OWNER                   | IT OWNER               | ENVIRONMENT                      | WORKFLOW EXECUTION          | CURRENT STAGE |
| myaacoub@microsoft.com           | myaacoub@microsoft.com | Dev                              | Human review at every stage | Deploy        |
| AZURE DEVOPS                     | ADO VISIBILITY         | GITHUB REPO                      | GITHUB VISIBILITY           |               |
| Fleet Inspection And Maintenance | private                | fleet-inspection-and-maintenance | public                      |               |

**Agent models**

Global defaults are inherited unless this project overrides an agent. Changes apply to future runs and revisions.

0 overrides

|                                                        |                          |                                         |
|--------------------------------------------------------|--------------------------|-----------------------------------------|
| <input type="checkbox"/> Requirements Agent            | Inherited global default | model-router (balanced: cost + quality) |
| <input type="checkbox"/> Planning Agent                | Inherited global default | model-router (balanced: cost + quality) |
| <input type="checkbox"/> Architecture Advisor Agent    | Inherited global default | gpt-5.4                                 |
| <input type="checkbox"/> Code Generation Agent         | Inherited global default | gpt-5.1-codex                           |
| <input type="checkbox"/> Test Planning Agent           | Inherited global default | model-router (balanced: cost + quality) |
| <input type="checkbox"/> Testing Agent                 | Inherited global default | gpt-5.1-codex                           |
| <input type="checkbox"/> Test Automation Agent         | Inherited global default | gpt-5.1-codex                           |
| <input type="checkbox"/> Security and Compliance Agent | Inherited global default | gpt-5.4                                 |
| <input type="checkbox"/> DevOps / Release Agent        | Inherited global default | gpt-5.4                                 |

The workflow panel shows ordered agent state, named Foundry identity, prerequisite, publication gate, last run, and whether each checkpoint is human or automated.

**Agentic SDLC — Software Factory**

**Michael Yaacoub**  
App Owner
  Sign out

**Agentic SDLC**  
Software Factory

AGENTIC SDLC OPERATIONS ▾

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN ▾

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION ▾

Overview

Architecture

| Agent                    | Inherited global default                                  | gpt-5.1-codex                             |
|--------------------------|-----------------------------------------------------------|-------------------------------------------|
| <input type="checkbox"/> | Test Automation Agent<br>Inherited global default         | gpt-5.1-codex ▾                           |
| <input type="checkbox"/> | Security and Compliance Agent<br>Inherited global default | gpt-5.4 ▾                                 |
| <input type="checkbox"/> | DevOps / Release Agent<br>Inherited global default        | gpt-5.4 ▾                                 |
| <input type="checkbox"/> | Ops Monitoring Agent<br>Inherited global default          | model-router (balanced: cost + quality) ▾ |
| <input type="checkbox"/> | Knowledge Assistant<br>Inherited global default           | model-router (balanced: cost + quality) ▾ |
| <input type="checkbox"/> | Insights Agent<br>Inherited global default                | model-router (balanced: cost + quality) ▾ |

Save project models

### 12-agent SDLC workflow

Named Microsoft Foundry agents run automatically through APIM. The selected execution policy controls where the workflow pauses.

• 12 agents

|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |                                                                                                                                                                                                                                                                                                               |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <div style="display: flex; align-items: center;"> <div style="margin-left: 10px;"> <b>1. Requirements Agent</b><br/>           Agent action · plan · 010-requirements-agent         </div> </div> <div style="display: flex; justify-content: space-between; align-items: center; margin-top: 5px;"> <div style="background-color: #d4edda; border-radius: 10px; padding: 2px 5px; font-weight: bold;">Published</div> <div>Last run 8/27/26, 4:06 AM</div> </div>                   | <div style="display: flex; align-items: center;"> <div style="margin-left: 10px;"> <b>Human checkpoint</b><br/>           Backlog Generation Approval - after Plan and Scope Approval         </div> </div> <div style="margin-top: 5px;">Backlog Generation Approval is already approved</div>               |
| <div style="display: flex; align-items: center;"> <div style="margin-left: 10px;"> <b>2. Planning Agent</b><br/>           Agent action · plan · 020-planning-agent         </div> </div> <div style="display: flex; justify-content: space-between; align-items: center; margin-top: 5px;"> <div style="background-color: #d4edda; border-radius: 10px; padding: 2px 5px; font-weight: bold;">Published</div> <div>Last run 8/27/26, 4:10 AM</div> </div>                           | <div style="display: flex; align-items: center;"> <div style="margin-left: 10px;"> <b>Human checkpoint</b><br/>           Backlog Generation Approval - after Plan and Scope Approval         </div> </div> <div style="margin-top: 5px;">Backlog Generation Approval is already approved</div>               |
| <div style="display: flex; align-items: center;"> <div style="margin-left: 10px;"> <b>3. Architecture Advisor Agent</b><br/>           Agent action · design · 030-architecture-advisor-agent         </div> </div> <div style="display: flex; justify-content: space-between; align-items: center; margin-top: 5px;"> <div style="background-color: #d4edda; border-radius: 10px; padding: 2px 5px; font-weight: bold;">Published</div> <div>Last run 8/27/26, 4:15 AM</div> </div> | <div style="display: flex; align-items: center;"> <div style="margin-left: 10px;"> <b>Human checkpoint</b><br/>           Architecture and Design Approval - after Backlog Generation Approval         </div> </div> <div style="margin-top: 5px;">Architecture and Design Approval is already approved</div> |
| <div style="display: flex; align-items: center;"> <div style="margin-left: 10px;"> <b>4. Code Generation Agent</b><br/>           Agent action · build · 040-code-generation-agent         </div> </div> <div style="display: flex; justify-content: space-between; align-items: center; margin-top: 5px;"> <div style="background-color: #d4edda; border-radius: 10px; padding: 2px 5px; font-weight: bold;">Published</div> <div>Last run 8/27/26, 4:17 AM</div> </div>            | <div style="display: flex; align-items: center;"> <div style="margin-left: 10px;"> <b>Human checkpoint</b><br/>           Code Generation Approval - after Architecture and Design Approval         </div> </div> <div style="margin-top: 5px;">Code Generation Approval is already approved</div>            |
| <div style="display: flex; align-items: center;"> <div style="margin-left: 10px;"> <b>5. Test Planning Agent</b><br/>           Agent action · test · 050-test-planning-agent         </div> </div> <div style="display: flex; justify-content: space-between; align-items: center; margin-top: 5px;"> <div style="background-color: #d4edda; border-radius: 10px; padding: 2px 5px; font-weight: bold;">Published</div> <div>Last run 8/27/26, 4:21 AM</div> </div>                 | <div style="display: flex; align-items: center;"> <div style="margin-left: 10px;"> <b>Human checkpoint</b><br/>           Test Acceptance Approval - after Code Generation         </div> </div> <div style="margin-top: 5px;">Test Acceptance Approval is already approved</div>                             |

The review workspace lets an approver include or exclude artifacts, edit proposal text, expand work-item trees, select exact rows, add/remove items, save drafts, approve and publish, request changes, reject, or delegate.



Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

8. Security and Compliance Agent

Agent action · security · 080-security-compliance-agent

Published

Last run 8/27/26, 4:27 AM

9. DevOps / Release Agent

Agent action · deploy · 090-devops-release-agent

Awaiting approval

Last run 8/27/26, 9:23 AM

10. Ops Monitoring Agent

Agent action · operate · 100-ops-monitoring-agent

Waiting

11. Knowledge Assistant

Agent action · operate · 110-knowledge-assistant

Waiting

12. Insights Agent

Agent action · improve · 120-insights-agent

Waiting

Human checkpoint

Security Review Approval · after Test Acceptance Approval

Security Review Approval is already approved

Human checkpoint

Release and Deployment Approval · after Pull Request Review Approval + Security Review Approval

Review & approve

Human checkpoint

Operate and Improve Approval · after Release and Deployment Approval

Waiting for approval: Release and Deployment Approval

Automated checkpoint

Advisory · no publication gate · after Release and Deployment Approval

Waiting for approval: Release and Deployment Approval

Human checkpoint

Operate and Improve Approval · after Release and Deployment Approval

Waiting for approval: Release and Deployment Approval

Human review workspace

Edit proposals and select exactly what can be published. Saving never writes to ADO or GitHub.

1 awaiting review

Include in approval

DevOps / Release Agent

Awaiting Approval

Approve & publish

Proposal title

DevOps / Release Agent output

Editable proposal

# DevOps / Release Agent — Deploy-Stage Reviewable Proposal

\*\*Project:\*\* Fleet Inspection And Maintenance

Summary view

Show full proposal

Expand all

Collapse all

Select all

Clear all

Add work item

Remove selected

## Minimal

Minimal policy pauses only at consequential checkpoints and automatically advances routine evidence gates. Field Service Work Orders is shown waiting at release after earlier routine checks advanced.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

← Existing projectsAwaitingApprovalDelete project

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Field service Work Orders

No description

Overview

Intake details captured when the project was created.

BUSINESS OWNERmyaacoub@microsoft.com

IT OWNERmyaacoub@microsoft.com

ENVIRONMENTDev

WORKFLOW EXECUTIONMinimal human intervention

CURRENT STAGEDeploy

AZURE DEVOPSField Service Work Orders

ADO VISIBILITYprivate

GITHUB REPOfield-service-work-orders

GITHUB VISIBILITYpublic

Agent models

Global defaults are inherited unless this project overrides an agent. Changes apply to future runs and revisions.

0 overrides

Requirements Agent

Inherited global default

model-router (balanced: cost + quality)

Planning Agent

Inherited global default

model-router (balanced: cost + quality)

Architecture Advisor Agent

Inherited global default

gpt-5.4

Code Generation Agent

Inherited global default

gpt-5.1-codex

Test Planning Agent

Inherited global default

model-router (balanced: cost + quality)

Testing Agent

Inherited global default

gpt-5.1-codex

Test Automation Agent

Inherited global default

gpt-5.1-codex

Security and Compliance Agent

Inherited global default

gpt-5.4

DevOps / Release Agent

Inherited global default

gpt-5.4

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

12-agent SDLC workflow

Named Microsoft Foundry agents run automatically through APIM. The selected execution policy controls where the workflow pauses.

12 agents

1. Requirements Agent

Agent action · plan · 010-requirements-agent

Published

Last run 8/27/26, 4:06 AM

Human checkpoint

Backlog Generation Approval · after Plan and Scope Approval

Backlog Generation Approval is already approved

2. Planning Agent

Agent action · plan · 020-planning-agent

Published

Last run 8/27/26, 4:08 AM

Human checkpoint

Backlog Generation Approval · after Plan and Scope Approval

Backlog Generation Approval is already approved

3. Architecture Advisor Agent

Agent action · design · 030-architecture-advisor-agent

Published

Last run 8/27/26, 4:13 AM

Human checkpoint

Architecture and Design Approval · after Backlog Generation Approval

Architecture and Design Approval is already approved

4. Code Generation Agent

Agent action · build · 040-code-generation-agent

Published

Last run 8/27/26, 4:16 AM

Automated checkpoint

Code Generation Approval · after Architecture and Design Approval

Code Generation Approval is already approved

5. Test Planning Agent

Agent action · test · 050-test-planning-agent

Published

Last run 8/27/26, 4:19 AM

Automated checkpoint

Test Acceptance Approval · after Code Generation Approval

Test Acceptance Approval is already approved

6. Testing Agent

Agent action · test · 060-testing-agent

Published

Last run 8/27/26, 4:21 AM

Automated checkpoint

Test Acceptance Approval · after Code Generation Approval

Test Acceptance Approval is already approved

7. Test Automation Agent

Agent action · test · 070-test-automation-agent

Published

Last run 8/27/26, 4:22 AM

Automated checkpoint

Test Acceptance Approval · after Code Generation Approval

Test Acceptance Approval is already approved

8. Security and Compliance Agent

Agent action · security · 080-security-compliance-agent

Published

Last run 8/27/26, 4:28 AM

Automated checkpoint

Security Review Approval · after Test Acceptance Approval

Security Review Approval is already approved

9. DevOps / Release Agent

Agent action · deploy · 090-devops-release-agent

Awaiting approval

Last run 8/27/26, 4:29 AM

Human checkpoint

Release and Deployment Approval · after Pull Request Review Approval + Security Review Approval

Review & approve

10. Ops Monitoring Agent

Agent action · operate · 100-ops-monitoring-agent

Waiting

Automated checkpoint

Operate and Improve Approval · after Release and Deployment Approval

Waiting for approval: Release and Deployment Approval

The same editing and evidence controls remain available at the human checkpoints retained by Minimal policy.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Human review workspace

Edit proposals and select exactly what can be published. Saving never writes to ADO or GitHub.

1 awaiting review

Include in approval

DevOps / Release Agent

Awaiting Approval

Approve & publish

Proposal title

DevOps / Release Agent output

Editable proposal

# DevOps / Release Agent — Deploy-Stage Reviewable Proposal

\*\*Project:\*\* Field service Work Orders

Summary view

Show full proposal

Expand all

Collapse all

Select all

Clear all

+ Add work item

Remove selected

Section

DevOps / Release Agent — Deploy-Stage Reviewable Proposal

Section

1. Deploy-stage recommendation summary

Section

Recommended deploy-stage outcome

3 of 3 items selected

Save draft

Release and Deployment Approval

1 proposal(s) selected for publication

1 Review

Select the items to publish

2 Decide

Approve or return with comments

3 Proceed

Publish and unlock the next agent

Decision comment

Required when requesting changes

## Autonomous

Autonomous policy runs the same agents and evidence checks with system-recorded gate decisions. It does not bypass guardrails, server authorization, APIM, external-system verification, or audit.

Agentic SDLC — Fully Autonomous Workflow

AUTOMATIC —

0 human checkpoints

1. Input & Design

Project Intake

010 Requirements Agent

G1 Plan & Scope

020 Planning Agent

G2 Backlog

030 Architecture Advisor Agent

G3 Architecture

040 Code Generation Agent

G4 Code

2. Build & Test

050 Test Planning Agent

G5 Pull Request

060 Testing Agent

G6 Test Acceptance

070 Test Automation Agent

G7 Security

080 Security & Compliance Agent

3. Release & Operate

090 DevOps / Release Agent

G8 Release

100 Ops Monitoring Agent

G9 Operate & Improve

110 Knowledge Assistant

120 Insights Agent

COMPLETE

Improvement backlog

Evidence validated → gate recorded automatically → next eligible agent starts

Michael Yaacoub | Sr Solution Engineer

Equipment Calibration Compliance demonstrates a completed autonomous run.

Agentic SDLC — Software Factory

Agentic SDLC  
Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Equipment Calibration Compliance

Existing projects

Complete

Delete project

Overview

Intake details captured when the project was created.

|                                  |                        |                                  |                    |               |
|----------------------------------|------------------------|----------------------------------|--------------------|---------------|
| BUSINESS OWNER                   | IT OWNER               | ENVIRONMENT                      | WORKFLOW EXECUTION | CURRENT STAGE |
| myaacoub@microsoft.com           | myaacoub@microsoft.com | Dev                              | Fully autonomous   | Improve       |
| AZURE DEVOPS                     | ADO VISIBILITY         | GITHUB REPO                      | GITHUB VISIBILITY  |               |
| Equipment Calibration Compliance | private                | equipment-calibration-compliance | public             |               |

Agent models

Global defaults are inherited unless this project overrides an agent. Changes apply to future runs and revisions.

0 overrides

|                          |                               |                          |                                         |
|--------------------------|-------------------------------|--------------------------|-----------------------------------------|
| <input type="checkbox"/> | Requirements Agent            | Inherited global default | model-router (balanced: cost + quality) |
| <input type="checkbox"/> | Planning Agent                | Inherited global default | model-router (balanced: cost + quality) |
| <input type="checkbox"/> | Architecture Advisor Agent    | Inherited global default | gpt-5.4                                 |
| <input type="checkbox"/> | Code Generation Agent         | Inherited global default | gpt-5.1-codex                           |
| <input type="checkbox"/> | Test Planning Agent           | Inherited global default | model-router (balanced: cost + quality) |
| <input type="checkbox"/> | Testing Agent                 | Inherited global default | gpt-5.1-codex                           |
| <input type="checkbox"/> | Test Automation Agent         | Inherited global default | gpt-5.1-codex                           |
| <input type="checkbox"/> | Security and Compliance Agent | Inherited global default | gpt-5.4                                 |
| <input type="checkbox"/> | DevOps / Release Agent        | Inherited global default | gpt-5.4                                 |

All 12 agents complete in order; checkpoints are labeled automated rather than awaiting a human action.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

12-agent SDLC workflow

Named Microsoft Foundry agents run automatically through APIM. The selected execution policy controls where the workflow pauses.

12 agents

|                                                                                                                |                                                            |                                                                                             |                                       |
|----------------------------------------------------------------------------------------------------------------|------------------------------------------------------------|---------------------------------------------------------------------------------------------|---------------------------------------|
| <div>1. Requirements Agent</div> <div>Agent action · plan · 010-requirements-agent</div>                       | <div>Published</div> <div>Last run 8/27/26, 4:06 AM</div>  | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>2. Planning Agent</div> <div>Agent action · plan · 020-planning-agent</div>                               | <div>Published</div> <div>Last run 8/27/26, 4:10 AM</div>  | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>3. Architecture Advisor Agent</div> <div>Agent action · design · 030-architecture-advisor-agent</div>     | <div>Published</div> <div>Last run 8/27/26, 4:14 AM</div>  | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>4. Code Generation Agent</div> <div>Agent action · build · 040-code-generation-agent</div>                | <div>Published</div> <div>Last run 8/27/26, 4:15 AM</div>  | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>5. Test Planning Agent</div> <div>Agent action · test · 050-test-planning-agent</div>                     | <div>Published</div> <div>Last run 8/27/26, 4:18 AM</div>  | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>6. Testing Agent</div> <div>Agent action · test · 060-testing-agent</div>                                 | <div>Published</div> <div>Last run 8/27/26, 4:20 AM</div>  | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>7. Test Automation Agent</div> <div>Agent action · test · 070-test-automation-agent</div>                 | <div>Published</div> <div>Last run 8/27/26, 4:21 AM</div>  | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>8. Security and Compliance Agent</div> <div>Agent action · security · 080-security-compliance-agent</div> | <div>Published</div> <div>Last run 8/27/26, 4:22 AM</div>  | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>9. DevOps / Release Agent</div> <div>Agent action · deploy · 090-devops-release-agent</div>               | <div>Published</div> <div>Last run 8/27/26, 4:23 AM</div>  | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>10. Ops Monitoring Agent</div> <div>Agent action · operate · 100-ops-monitoring-agent</div>               | <div>Published</div> <div>Last run 8/27/26, 10:27 AM</div> | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |

Completed projects can start a traceable revision from Requirements, Planning/Work Items, or Architecture. Revision instructions enter all downstream prompts; valid prior approvals are carried forward and a new run is created.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Revise completed workflow

Start a traceable revision from an earlier stage and continue automatically under this project's execution policy.

New workflow run

Restart from

Requirements

Revision instructions

Describe what must change and why

Published artifacts remain the baseline; the new run records carried-forward policy checkpoints and revised outputs.

Start revision

12-agent SDLC workflow

Named Microsoft Foundry agents run automatically through APIM. The selected execution policy controls where the workflow pauses.

12 agents

|                                                                                                            |                                                           |                                                                                             |                                       |
|------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------|---------------------------------------------------------------------------------------------|---------------------------------------|
| <div>1. Requirements Agent</div> <div>Agent action · plan · 010-requirements-agent</div>                   | <div>Published</div> <div>Last run 8/27/26, 4:06 AM</div> | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>2. Planning Agent</div> <div>Agent action · plan · 020-planning-agent</div>                           | <div>Published</div> <div>Last run 8/27/26, 4:10 AM</div> | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>3. Architecture Advisor Agent</div> <div>Agent action · design · 030-architecture-advisor-agent</div> | <div>Published</div> <div>Last run 8/27/26, 4:14 AM</div> | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>4. Code Generation Agent</div> <div>Agent action · build · 040-code-generation-agent</div>            | <div>Published</div> <div>Last run 8/27/26, 4:15 AM</div> | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>5. Test Planning Agent</div> <div>Agent action · test · 050-test-planning-agent</div>                 | <div>Published</div> <div>Last run 8/27/26, 4:18 AM</div> | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>6. Testing Agent</div> <div>Agent action · test · 060-testing-agent</div>                             | <div>Published</div> <div>Last run 8/27/26, 4:20 AM</div> | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |
| <div>7. Test Automation Agent</div> <div>Agent action · test · 070-test-automation-agent</div>             | <div>Published</div> <div>Last run 8/27/26, 4:21 AM</div> | <div>Automated checkpoint</div> <div>Workflow policy · after prior policy checkpoints</div> | <div>Policy checkpoint complete</div> |

# Project Details workspace

Project Details is the primary project command center.

## Provisioned systems

This section links the ADO project and GitHub repository and surfaces provisioning status, visibility, reason, and actionable failure detail.

The screenshot displays the 'Project Details workspace' for 'Agentic SDLC — Software Factory'. The interface includes a top navigation bar with the user 'Michael Yaacoub' (App Owner) and a 'Sign out' button. A left sidebar contains navigation links for 'AGENTIC SDLC OPERATIONS' (Dashboard, New Project, New Project Set, Existing Projects, Deleted Projects, Workflow Runs, Human Approval Queue, Agent Activity, Audit Trail) and 'ADMIN' (User Management, Project Access, Role Permissions, Agent Configuration, Global Settings, APIM & Config). The main content area is titled 'Section 2. Deployment context interpreted from supplied artifacts' and shows '3 of 3 items selected' with a 'Save draft' button. The first section, 'Release and Deployment Approval', indicates '1 proposal(s) selected for publication' and is in an 'Awaiting Approval' state. It features a three-step process: 1. Review (Select the items to publish), 2. Decide (Approve or return with comments), and 3. Proceed (Publish and unlock the next agent). A 'Decision comment' field is present with the text 'Required when requesting changes'. Below this, a note states 'Approval is the only action that publishes to ADO or GitHub.' with buttons for 'Request changes' and 'Save & approve selected'. The second section, 'Provisioned systems of record', notes it was 'Created when the project was submitted. Retry after adding a missing credential.' and includes a 'Retry provisioning' button. It lists two systems: 'Azure DevOps project' (existing, private) with URL 'https://dev.azure.com/csdmichael/Fleet%20Inspection%20And%20Maintenance', and 'GitHub repository' (existing, public) with URL 'https://github.com/csdmichael/fleet-inspection-and-maintenance'. The third section, 'Lifecycle', states 'Stage order is fixed; each transition needs its approval gate.'

## Lifecycle

Lifecycle shows stage progression and the current run state from planning through improvement.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

> ☒ Section 2. Deployment context interpreted from supplied artifacts

3 of 3 items selectedSave draft

Release and Deployment Approval

1 proposal(s) selected for publication

1 Review

Select the items to publish

2 Decide

Approve or return with comments

3 Proceed

Publish and unlock the next agent

Decision comment

Required when requesting changes

Approval is the only action that publishes to ADO or GitHub.

Request changes

Save & approve selected

Provisioned systems of record

Created when the project was submitted. Retry after adding a missing credential.

Retry provisioning

Azure DevOps project

existingprivate

Fleet Inspection And Maintenance

<https://dev.azure.com/csdmichael/Fleet%20Inspection%20And%20Maintenance>

GitHub repository

existingpublic

fleet-inspection-and-maintenance

<https://github.com/csdmichael/fleet-inspection-and-maintenance>

Lifecycle

Stage order is fixed; each transition needs its approval gate.

## Approval gates

The gates section shows role, state, evidence ownership, decisions, comments, delegation, and prerequisites for all nine checkpoints.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

https://github.com/csdmichael/fleet-inspection-and-maintenance

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Lifecycle

Stage order is fixed; each transition needs its approval gate.

Plan

Design

Build

Test

Security

Deploy

Operate

Improve

Approval gates

9 gate(s) - decisions are recorded on the audit trail.

Decision comment (optional)  
Explain the decision for the audit record

Delegate review to  
person@company.com or team name

| GATE                             | STAGE  | REQUIRES      | LAST DECISION                        | ARTIFACTS                            | STATUS   | ACTIONS   |
|----------------------------------|--------|---------------|--------------------------------------|--------------------------------------|----------|-----------|
| Plan and Scope Approval          | Plan   | business_user | approve<br>by myaacoub@microsoft.com | Not required                         | Approved | No action |
| Architecture and Design Approval | Design | it_user       | approve<br>by myaacoub@microsoft.com | Architecture Advisor Agent           | Approved | No action |
| Backlog Generation Approval      | Plan   | business_user | approve<br>by myaacoub@microsoft.com | Requirements Agent<br>Planning Agent | Approved | No action |

## Systems of Record

This section resolves each effective provider and indicates whether the value is inherited globally or overridden for the project.



Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Test Acceptance Approval

Test

it\_user

approve  
by myaacob@microsoft.com

Test Planning Agent

Testing Agent

Test Automation Agent

Approved

No action

Release and Deployment Approval

Deploy

it\_user

—

DevOps / Release Agent

Awaiting Approval

Approve & publish

Request changes

Reject

Delegate

Operate and Improve Approval

Improve

business\_user

—

Generate proposal first

Awaiting Approval

Approve & publish

Request changes

Reject

Delegate

Systems of Record

Inherited from global settings unless overridden here.

5 items

Generated assets

Everything the agents created in Azure DevOps and GitHub. Links open in a new tab.

49 items

Agent runs & artifacts

9 run(s) · 9 artifact(s)

18 items

## Generated assets

Generated Assets groups links by system and category: ADO planning/test/release assets, GitHub repository/PR/commits/docs, Azure applications, and other published evidence.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Test Acceptance Approval

Test

it\_user

approve  
by myaacoub@microsoft.com

Test Planning Agent

Testing Agent

Test Automation Agent

Approved

No action

Release and Deployment Approval

Deploy

it\_user

—

DevOps / Release Agent

Awaiting Approval

Approve & publish

Request changes

Reject

Delegate

Operate and Improve Approval

Improve

business\_user

—

Generate proposal first

Awaiting Approval

Approve & publish

Request changes

Reject

Delegate

Systems of Record

Inherited from global settings unless overridden here.

5 items

Generated assets

Everything the agents created in Azure DevOps and GitHub. Links open in a new tab.

49 items

Agent runs & artifacts

9 run(s) · 9 artifact(s)

18 items

## Agent runs and artifacts

This trace view correlates each prompt agent, model, timing, outcome, proposal artifact, and verified tool call.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Test Acceptance Approval

Test

it\_user

approve  
by myaacoub@microsoft.com

Test Planning Agent

Testing Agent

Test Automation Agent

Approved

No action

Release and Deployment Approval

Deploy

it\_user

—

DevOps / Release Agent

Awaiting Approval

Approve & publish

Request changes

Reject

Delegate

Operate and Improve Approval

Improve

business\_user

—

Generate proposal first

Awaiting Approval

Approve & publish

Request changes

Reject

Delegate

Systems of Record

Inherited from global settings unless overridden here.

5 items

Generated assets

Everything the agents created in Azure DevOps and GitHub. Links open in a new tab.

49 items

Agent runs & artifacts

9 run(s) · 9 artifact(s)

18 items

## Operational screens

### Workflow Runs

Workflow Runs provides cross-project execution status, automation state, progress, active task, policy, timestamps, and failure context.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Workflow Runs

Every Agent Framework run, with its current lifecycle stage and state.

| RUN      | CURRENT STAGE | STAGES | CREATED                  | STATUS            |
|----------|---------------|--------|--------------------------|-------------------|
| f8f00af8 | Deploy        | 8      | Aug 27, 2026, 4:05:44 AM | Awaiting Approval |
| f0d3c72e | Deploy        | 8      | Aug 27, 2026, 4:05:27 AM | Awaiting Approval |
| 4e7cc372 | Improve       | 8      | Aug 27, 2026, 4:05:09 AM | Approved          |
| bc3f46da | Improve       | 8      | Aug 27, 2026, 4:04:52 AM | Approved          |

## Human Approval Queue

The queue consolidates actionable gates across projects. Open a row to review the corresponding proposal in Project Details.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Human Approval Queue

Gates awaiting a human decision. You can only act on gates your role is authorized for — the API re-checks every decision.

Pending gates

3 awaiting a decision

Decision comment (optional)

Recorded on the audit trail with your decision

| GATE                                                | STAGE   | REQUIRED ROLE | STATUS            | DECISION                            |
|-----------------------------------------------------|---------|---------------|-------------------|-------------------------------------|
| Release and Deployment Approval<br>Project 4354d086 | Deploy  | it_user       | Awaiting Approval | <div>ApproveChangesRejectOpen</div> |
| Release and Deployment Approval<br>Project 0876fc39 | Deploy  | it_user       | Awaiting Approval | <div>ApproveChangesRejectOpen</div> |
| Operate and Improve Approval<br>Project 0876fc39    | Improve | business_user | Awaiting Approval | <div>ApproveChangesRejectOpen</div> |

## Agent Activity

Agent Activity is the operational trace of model runs and outputs. Use it to inspect agent identity, lifecycle stage, model, project, status, duration, and correlation data.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Agent Activity

Every agent run with its model, APIM route, token estimate, guardrail findings, and correlation ID.

| AGENT                                                                                                                                                                                                                                                                                                                                                                                                                                       | MODEL & ROUTE                                                                                                 | TOKENS | GUARDRAILS       | STARTED                               | STATUS         |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------|--------|------------------|---------------------------------------|----------------|
| <div>insights-agent</div> <div># Insights Agent — Improve-Stage Proposal **Project:** Equipment Calibration Compliance **Target environment:** Dev **Date:** 27 August 2026 **Status:** **Proposed for human review; no implementation or production change authorized** ## 1. Evidence assessment ### Evidence available - Requirements, technical requirements, and UX documents dated **24 August 2026**, all marked **Draft v1.0*</div> | model-router<br>foundry-<br>agents{projectPath}/agents/{foundryAgentName}/endpoint/protocols/openai/responses | 6820   | <div>Clean</div> | 8/27/26, 10:29 AM<br>corr<br>4912c420 | <div>Com</div> |
| <div>knowledge-assistant</div> <div># Operate-stage proposal — Equipment Calibration Compliance **Target environment:** Dev **Proposal status:** For human review and approval; no deployment, configuration, or external-system change has been performed. **Operating objective:** Validate that the Dev solution</div>                                                                                                                   | model-router<br>foundry-<br>agents{projectPath}/agents/{foundryAgentName}/endpoint/protocols/openai/responses | 6821   | <div>Clean</div> | 8/27/26, 10:28 AM<br>corr<br>4912c420 | <div>Com</div> |

## Audit Trail

Audit Trail is append-only evidence for user, system, workflow, connector, publication, access, and administration actions. Filters support investigation by action, target, actor, and correlation ID.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Audit Trail

Append-only record of user actions, agent actions, and approval decisions.

Filter by action, actor, or target

200 of 200

| ACTOR                                                               | ACTION                     | TARGET                      | WHEN                     | CORRELATION |
|---------------------------------------------------------------------|----------------------------|-----------------------------|--------------------------|-------------|
| <div>• user</div> <div>admin@mngenvmcap829495.onmicrosoft.com</div> | project.delete             | project<br>8a94afac-e7e     | Aug 27, 2026, 8:17:56 PM | 94b974fc    |
| <div>• system</div> <div>workflow-automation</div>                  | workflow.automation.failed | workflowRun<br>154dbce3-1fc | Aug 27, 2026, 8:17:55 PM | cf346e9b    |
| <div>• system</div> <div>workflow-automation</div>                  | workflow.automation.queued | workflowRun<br>154dbce3-1fc | Aug 27, 2026, 8:17:38 PM | cf346e9b    |
| <div>• system</div> <div>workflow-automation</div>                  | workflow.automation.queued | workflowRun<br>154dbce3-1fc | Aug 27, 2026, 8:17:20 PM | cf346e9b    |
| <div>• system</div> <div>workflow-automation</div>                  | workflow.automation.queued | workflowRun<br>154dbce3-1fc | Aug 27, 2026, 8:17:02 PM | cf346e9b    |
| <div>• user</div> <div>admin@mngenvmcap829495.onmicrosoft.com</div> | project.delete             | project<br>4fb71868-e33     | Aug 27, 2026, 8:16:45 PM | 1a6f01c0    |
| <div>• system</div> <div>workflow-automation</div>                  | workflow.automation.queued | workflowRun<br>154dbce3-1fc | Aug 27, 2026, 8:16:44 PM | cf346e9b    |
| <div>• system</div> <div>workflow-automation</div>                  | workflow.automation.queued | workflowRun<br>154dbce3-1fc | Aug 27, 2026, 8:16:27 PM | cf346e9b    |
| <div>• user</div> <div>admin@mngenvmcap829495.onmicrosoft.com</div> | project.delete             | project<br>97068385-317     | Aug 27, 2026, 8:16:26 PM | a40210dc    |

## Email notifications

Azure Communication Services sends lifecycle email to deduplicated Business and IT Owners. Persistent notification records make delivery idempotent across retries and API restarts. Notifications are emitted when:

- A project is created, including execution mode, environment, creator, and a link back to the Factory.
- A workflow reaches an actionable human approval gate.
- A workflow fails and requires operator attention.
- A project completes its full lifecycle.
- Project Access grants or removes managed Factory, ADO, and optional GitHub access.

The Project Access email groups Factory, Azure DevOps, and GitHub destinations into one message and copies the configured audit recipient. When GitHub username is blank, GitHub access and GitHub-specific email copy are omitted.

## [EXTERNAL] Agentic SDLC project access granted

Summarize



DoNotReply <DoNotReply@0bfc94cf-1ab6-4c

To Vinay Gandhi

Cc Michael Yaacoub



Reply



Reply All



Forward



Thu 8/27/2026 2:55 PM

This sender DoNotReply@0bfc94cf-1ab6-4c16-8f42-c68b13422539.us2.azurecomm.net is from outside your organization.

You now have administrator access to the Agentic SDLC Factory and contributor access to the projects listed below.

SDLC Factory: <https://nam06.safelinks.protection.outlook.com/?url=https%3A%2F%2Fagentic-sdlc-ui-my.azurewebsites.net%2F&data=05%7C02%7Cmyaacoub%40microsoft.com%7Ceb87fb4d286f45c6982b08df0485d9cd%7C72f988bf86f141af91ab2d7cd011db47%7C1%7C0%7C639234645516256298%7CUnknown%7CTWFpbGZsb3d8eyJFbXB0eU1hcGkiOnRydWUsIlYiOiIwLjAuMDAwMCIslAI0iXaW4zMlslkFOljoITWFpbCIsIldUljoyfQ%3D%3D%7C60000%7C%7C%7C&sdata=fMbtAPzXMW1k0lPbJh91QJaWcbUSXmEI1beO3XJxp8%3D&reserved=0>

### Azure DevOps projects:

- To do list: <https://nam06.safelinks.protection.outlook.com/?url=https%3A%2F%2Fdev.azure.com%2Fcsdmichael%2Fto%2520do%2520list&data=05%7C02%7Cmyaacoub%40microsoft.com%7Ceb87fb4d286f45c6982b08df0485d9cd%7C72f988bf86f141af91ab2d7cd011db47%7C1%7C0%7C639234645516273037%7CUnknown%7CTWFpbGZsb3d8eyJFbXB0eU1hcGkiOnRydWUsIlYiOiIwLjAuMDAwMCIslAI0iXaW4zMlslkFOljoITWFpbCIsIldUljoyfQ%3D%3D%7C60000%7C%7C%7C&sdata=01XB22f7AyO7BFV2YmxX3FJ5jbEzq9t%2FD2plRx5J7ys%3D&reserved=0>

### GitHub repositories:

- To do list: <https://nam06.safelinks.protection.outlook.com/?url=https%3A%2F%2Fgithub.com%2Fcsdmichael%2Fto-do-list&data=05%7C02%7Cmyaacoub%40microsoft.com%7Ceb87fb4d286f45c6982b08df0485d9cd%7C72f988bf86f141af91ab2d7cd011db47%7C1%7C0%7C639234645516284064%7CUnknown%7CTWFpbGZsb3d8eyJFbXB0eU1hcGkiOnRydWUsIlYiOiIwLjAuMDAwMCIslAI0iXaW4zMlslkFOljoITWFpbCIsIldUljoyfQ%3D%3D%7C60000%7C%7C%7C&sdata=ug52r9kEoKW%2F%2FIH1xKqF1hZd1%2BLzM1vU%2FuKKxYPePAo%3D&reserved=0>

GitHub may require you to accept a collaborator invitation before repository access is active.

## Generated Azure DevOps assets

Native ADO browser capture was retried and reached an interactive password prompt. The following screenshots are therefore clearly labeled live evidence views generated from authenticated ADO REST responses. They contain actual project IDs, work-item IDs/states, sprint dates, query definitions, dashboard widget metadata, test records, wiki content, and repository records from Equipment Calibration Compliance.

### Backlog and work-item hierarchy

The Azure DevOps backlog publication created 76 work items: one Epic, nested Features, 12 User Stories, implementation Tasks, and test cases. Parent-child relationships and sprint assignment preserve traceability from scope to delivery.



# Azure DevOps backlog

Equipment Calibration Compliance

Azure DevOps project 680756e8-7ded-4202-b89e-5304ce1884c6

Captured 2026-08-28 03:30 UTC

**76**

Generated work items

**1**

Epics

**12**

User stories

**36**

Tasks

## Epic → Feature → User Story → Task hierarchy

| ID  | Work item                                                                           | State  | Iteration                                 |
|-----|-------------------------------------------------------------------------------------|--------|-------------------------------------------|
| 650 | <b>Epic</b> Equipment Calibration Compliance delivery                               | Closed | Equipment Calibration Compliance          |
| 651 | <b>Feature</b> Planning Proposal — Equipment Calibration Compliance                 | Closed | Equipment Calibration Compliance\Sprint 1 |
| 652 | <b>User Story</b> Instrument due and overdue visibility.                            | Closed | Equipment Calibration Compliance\Sprint 1 |
| 653 | <b>Task</b> Design: Instrument due and overdue visibility.                          | Closed | Equipment Calibration Compliance\Sprint 1 |
| 654 | <b>Task</b> Implement: Instrument due and overdue visibility.                       | Closed | Equipment Calibration Compliance\Sprint 1 |
| 655 | <b>Task</b> Test: Instrument due and overdue visibility.                            | Closed | Equipment Calibration Compliance\Sprint 1 |
| 656 | <b>User Story</b> Guided calibration capture with immutable as-found readings.      | Closed | Equipment Calibration Compliance\Sprint 1 |
| 657 | <b>Task</b> Design: Guided calibration capture with immutable as-found readings.    | Closed | Equipment Calibration Compliance\Sprint 1 |
| 658 | <b>Task</b> Implement: Guided calibration capture with immutable as-found readings. | Closed | Equipment Calibration Compliance\Sprint 1 |
| 659 | <b>Task</b> Test: Guided calibration capture with immutable as-found readings.      | Closed | Equipment Calibration Compliance\Sprint 1 |

Individual work items retain type, state, area, iteration, description, acceptance criteria, parent/child relationships, and hyperlinks to code, pull request, CI, and deployment evidence.

# Azure DevOps work item

Generated and lifecycle-linked planning evidence

[https://dev.azure.com/csdmichael/680756e8-7ded-4202-b89e-5304ce1884c6/\\_apis/wit/workitems/650](https://dev.azure.com/csdmichael/680756e8-7ded-4202-b89e-5304ce1884c6/_apis/wit/workitems/650)

Captured 2026-08-28 03:30 UTC

## Epic 650: Equipment Calibration Compliance delivery

| Field         | Value                                     |
|---------------|-------------------------------------------|
| ID            | 650                                       |
| Type          | Epic                                      |
| Title         | Equipment Calibration Compliance delivery |
| State         | Closed                                    |
| Assigned to   | Michael Yaacoub                           |
| Iteration     | Equipment Calibration Compliance          |
| Area          | Equipment Calibration Compliance          |
| Related links | 11                                        |

### Description

No description was supplied at intake. This epic is the delivery container for Equipment Calibration Compliance . It groups every feature, user story, and task the Agentic SDLC workflow derived from the approved requirements and UX mockups. Scope was approved by a human reviewer at the Requirements gate before any work item was created. Anything outside that approved scope belongs in a new epic rather than this one. Business owner: myaacoub@microsoft.com. IT owner: myaacoub@microsoft.com. Target environment: Dev. Source: Planning Agent output , produced by the Planning Agent and accepted at the approval gate on 2026-08-27.

### Acceptance criteria

Defined on child stories and tasks.

## Sprints

Planning creates three dated two-week iterations and subscribes the default team so sprint boards, capacity, burndown, and current-iteration queries work.

LIVE GENERATED EVIDENCE

### Azure DevOps sprints

Three generated two-week iterations

[https://dev.azure.com/csdmichael/Equipment%20Calibration%20Compliance/\\_sprints](https://dev.azure.com/csdmichael/Equipment%20Calibration%20Compliance/_sprints)

Captured 2026-08-28 03:30 UTC

Dated delivery iterations

| Sprint      | Start                | Finish               | Path                                                    |
|-------------|----------------------|----------------------|---------------------------------------------------------|
| Iteration 1 | —                    | —                    | \Equipment Calibration Compliance\iteration\Iteration 1 |
| Iteration 2 | —                    | —                    | \Equipment Calibration Compliance\iteration\Iteration 2 |
| Iteration 3 | —                    | —                    | \Equipment Calibration Compliance\iteration\Iteration 3 |
| Sprint 1    | 2026-08-27T00:00:00Z | 2026-09-09T00:00:00Z | \Equipment Calibration Compliance\iteration\Sprint 1    |
| Sprint 2    | 2026-09-10T00:00:00Z | 2026-09-23T00:00:00Z | \Equipment Calibration Compliance\iteration\Sprint 2    |
| Sprint 3    | 2026-09-24T00:00:00Z | 2026-10-07T00:00:00Z | \Equipment Calibration Compliance\iteration\Sprint 3    |

Evidence generated from live Azure DevOps or Azure Resource Manager APIs because interactive portal sign-in is not available to the unattended documentation browser.

## Shared queries

The generated Shared Queries cover all work, active stories, open bugs, test cases, current sprint, and agent-generated items. Dashboard tiles reuse these stable query IDs.

## Azure DevOps shared queries

Reusable views for delivery, testing, and progress

[https://dev.azure.com/csdmichael/Equipment%20Calibration%20Compliance/\\_queries](https://dev.azure.com/csdmichael/Equipment%20Calibration%20Compliance/_queries)

Captured 2026-08-28 03:30 UTC

### Shared Queries generated by Planning

| Query                 | Type | WQL |
|-----------------------|------|-----|
| All Work Items        | flat |     |
| Active User Stories   | flat |     |
| Open Bugs             | flat |     |
| Test Cases            | flat |     |
| Current Sprint Work   | flat |     |
| Agent Generated Items | flat |     |

Evidence generated from live Azure DevOps or Azure Resource Manager APIs because interactive portal sign-in is not available to the unattended documentation browser.

## Dashboards

The default Overview dashboard is populated with project links, delivery/testing context, and query-scalar widgets.

LIVE GENERATED EVIDENCE

## Azure DevOps Overview dashboard

Equipment Calibration Compliance

Dashboard ID 9310ecb7-01b6-4589-ab18-728205731bdc

Captured 2026-08-28 03:30 UTC

13

Widgets

**Equipment Calibration  
Compliance Team**

Team

**Overview**

Dashboard

**Live**

REST status

### Dashboard layout

#### New Work Item

NewWorkItemWidget

Position 5, 3

#### Current Sprint Work

QueryScalarWidget

Position 8, 3

#### Sprint Burndown

SprintBurndownWidget

Position 3, 1

#### Agent Generated Items

QueryScalarWidget

Position 8, 4

#### Active User Stories

QueryScalarWidget

Position 7, 4

#### Open Bugs

QueryScalarWidget

Position 8, 1

#### All Work Items

QueryScalarWidget

Position 7, 3

#### Sprint Capacity

SprintCapacityWidget

Position 3, 3

#### Test Cases

QueryScalarWidget

Position 8, 2

#### Assigned to me

AssignedToMeWidget

Position 5, 1

#### Sprint Overview

SprintOverviewWidget

Position 1, 3

#### Equipment Calibration Compliance

MarkdownWidget

Position 1, 1

A second Agentic SDLC dashboard provides workflow-focused delivery metrics.

LIVE GENERATED EVIDENCE

## Azure DevOps Agentic SDLC dashboard

Equipment Calibration Compliance

Dashboard ID 7bcd25d2-c591-4db1-8dea-26c21284bc3a

Captured 2026-08-28 03:30 UTC

7

Widgets

**Equipment Calibration  
Compliance Team**

Team

**Equipment Calibration  
Compliance**

Dashboard

**Live**

REST status

### Dashboard layout

#### Current Sprint Work

QueryScalarWidget

Position 2, 2

#### All Work Items

QueryScalarWidget

Position 1, 1

#### Agentic SDLC

MarkdownWidget

Position 4, 1

#### Open Bugs

QueryScalarWidget

Position 1, 3

#### Agent Generated Items

QueryScalarWidget

Position 2, 3

#### Active User Stories

QueryScalarWidget

Position 1, 2

#### Test Cases

QueryScalarWidget

Position 2, 1

Evidence generated from live Azure DevOps or Azure Resource Manager APIs because interactive portal sign-in is not available to the unattended documentation browser.

## Delivery plan

The delivery plan maps the team backlog across generated sprints and gives stakeholders a cross-iteration roadmap.

LIVE GENERATED EVIDENCE

**Azure DevOps delivery plan**  
Cross-sprint roadmap for generated work

Delivery plan ID 95e87a9e-b26f-4089-9cd7-3d62e269c3dc

Captured 2026-08-28 03:30 UTC

**Equipment Calibration Compliance delivery plan**  
Plan

**1**  
Team backlog mapping

**3**  
Sprints

**Live**  
REST status

**Delivery timeline configuration**

| Team                                 | Backlog category       | Work item type |
|--------------------------------------|------------------------|----------------|
| a53731e1-2e45-4207-af93-003d7c0fbb24 | Microsoft.EpicCategory |                |

Evidence generated from live Azure DevOps or Azure Resource Manager APIs because interactive portal sign-in is not available to the unattended documentation browser.

## Test plan and automated run

Test Planning publishes an idempotent plan and suites linked to requirement-derived cases.

LIVE GENERATED EVIDENCE

## Azure DevOps test plan

Traceable test suites and cases generated from requirements

Test plan ID 678

Captured 2026-08-28 03:30 UTC

**678**

Test plan ID

**1**

Suites

**Active**

State

**Automated**

Validation policy

### Equipment Calibration Compliance automated validation

| Suite ID | Suite                                                 | Type            | State  |
|----------|-------------------------------------------------------|-----------------|--------|
| 679      | Equipment Calibration Compliance automated validation | staticTestSuite | Active |

Evidence generated from live Azure DevOps or Azure Resource Manager APIs because interactive portal sign-in is not available to the unattended documentation browser.

Testing and Test Automation reuse exact-commit CI evidence, create a plan-linked ADO Test Run, set outcomes, and attach automation links. The captured run contains 15 passed results.

LIVE GENERATED EVIDENCE

## Azure DevOps automated test run

Pipeline-linked validation evidence

Test run ID 1000010

Captured 2026-08-28 03:30 UTC

**15**

Test results

**15**

Passed

**Completed**

Run state

**1000010**

Run ID

### Equipment Calibration Compliance automated run 33066697363

| Result | Test case                                                                                                                                      | Outcome | Duration ms |
|--------|------------------------------------------------------------------------------------------------------------------------------------------------|---------|-------------|
| 100000 | Calculates and presents calibration due and overdue instruments correctly.                                                                     | Passed  |             |
| 100001 | Prevents overdue instruments from being issued for use.                                                                                        | Passed  |             |
| 100002 | Enforces extension expiry, justification, and approver controls.                                                                               | Passed  |             |
| 100003 | Presents the approved procedure and valid reference standard.                                                                                  | Passed  |             |
| 100004 | Captures immutable as-found readings before as-left readings.                                                                                  | Passed  |             |
| 100005 | **Backend unit/integration:** pytest, FastAPI TestClient, SQLAlchemy fixtures (using SQLite in-memory or Azure SQL Edge container).            | Passed  |             |
| 100006 | **API contract & negative tests:** pytest + respx (HTTP mocking) + JSON Schema validation via 'pydantic'.                                      | Passed  |             |
| 100007 | **Frontend unit/component:** Angular 18 + Jest/Vitest + Testing Library; Ionic specific harness for service worker.                            | Passed  |             |
| 100008 | **End-to-end:** Playwright (TypeScript) with storage state per persona (Technician, Quality Manager). Supports mobile/tablet viewport configs. | Passed  |             |
| 100009 | **Accessibility helpers:** axe-core via Playwright for critical screens.                                                                       | Passed  |             |
| 100010 | Prevents overdue instruments from being issued or used.                                                                                        | Passed  |             |
| 100011 | Presents the approved procedure and captures complete calibration evidence.                                                                    | Passed  |             |
| 100012 | Makes as-found readings immutable and evaluates tolerance correctly.                                                                           | Passed  |             |

## Project wiki

The release agent publishes a Project Overview wiki page containing owners, stack, repository/PR/deployment evidence, hosted UI/API/health/Swagger links, governance context, and publication timestamp.

LIVE GENERATED EVIDENCE

### Azure DevOps project wiki

Generated Project Overview release documentation

Wiki ID ed512e5c-f960-4463-bc31-0d045523f6b6

Captured 2026-08-28 03:30 UTC

|                                                     |                                                  |                                                          |                                           |
|-----------------------------------------------------|--------------------------------------------------|----------------------------------------------------------|-------------------------------------------|
| <b>Project Overview</b><br><small>Wiki page</small> | <b>1696</b><br><small>Content characters</small> | <b>/Project%2DOverview.md</b><br><small>Git path</small> | <b>Published</b><br><small>Status</small> |
|-----------------------------------------------------|--------------------------------------------------|----------------------------------------------------------|-------------------------------------------|

#### Release and operating record

# Equipment Calibration Compliance

Not specified

## Hosted application

|                                                                                              |
|----------------------------------------------------------------------------------------------|
| Resource   URL                                                                               |
| ---   ---                                                                                    |
| Hosted UI   <https://equipment-calibration-compliance-ui.azurewebsites.net>                  |
| API   <https://equipment-calibration-compliance-api.azurewebsites.net>                       |
| API health   <https://equipment-calibration-compliance-api.azurewebsites.net/health>         |
| Swagger UI   <https://equipment-calibration-compliance-api.azurewebsites.net/docs>           |
| OpenAPI JSON   <https://equipment-calibration-compliance-api.azurewebsites.net/openapi.json> |

## Source and delivery

|                                                                                                 |
|-------------------------------------------------------------------------------------------------|
| Item   Value                                                                                    |
| ---   ---                                                                                       |
| GitHub repository   <https://github.com/csdmichael/equipment-calibration-compliance>            |
| Released pull request   <https://github.com/csdmichael/equipment-calibration-compliance/pull/2> |

## Azure Repos

The public GitHub repository is imported idempotently into Azure Repos after intake publication. Private GitHub repositories are skipped unless a suitable service connection is configured.

LIVE GENERATED EVIDENCE

## Azure Repos

Project source mirror and generated repository evidence

Azure DevOps project 680756e8-7ded-4202-b89e-5304ce1884c6

Captured 2026-08-28 03:30 UTC

1

Azure Repos

Imported

GitHub source policy

private

Project visibility

Live

REST status

### Generated and imported repositories

| Repository ID                        | Name                             | Default branch                    | Remote URL                                                                                                                 |
|--------------------------------------|----------------------------------|-----------------------------------|----------------------------------------------------------------------------------------------------------------------------|
| b054ee0b-82f5-4026-a900-71c685c541b5 | Equipment Calibration Compliance | refs/heads/feature/agent/43aa63a7 | https://csdmichael@dev.azure.com/csdmichael/Equipment%20Calibration%20Compliance/_git/Equipment%20Calibration%20Compliance |

Evidence generated from live Azure DevOps or Azure Resource Manager APIs because interactive portal sign-in is not available to the unattended documentation browser.

## Generated GitHub assets

GitHub screenshots are native public pages from the generated Equipment Calibration Compliance repository.

### Repository

Code Generation creates one repository with `ui/`, `api/`, `db/`, `docs/`, `.github/workflows/`, tests, configuration, license, and README.



PlatformSolutionsResourcesOpen SourceEnterprisePricing

Search / Sign in Sign up

csdmichael / equipment-calibration-compliance Public

Notifications Fork 0 Star 0

<> Code Issues Pull requests Actions Projects Security and quality Insights

main 3 Branches 0 Tags

Go to file Code

agentic-sdlc-release-agent[b... DevOps Release Agent: record published links [skip ci] 53c142b · 10 hours ago 19 Commits

|            |                                                               |              |
|------------|---------------------------------------------------------------|--------------|
| .github    | Equipment Calibration Compliance: generated application sc... | yesterday    |
| api        | Equipment Calibration Compliance: generated application sc... | yesterday    |
| db         | Equipment Calibration Compliance: generated application sc... | yesterday    |
| docs       | Equipment Calibration Compliance: generated application sc... | 10 hours ago |
| ui         | Equipment Calibration Compliance: generated application sc... | yesterday    |
| .gitignore | Equipment Calibration Compliance: generated application sc... | yesterday    |
| LICENSE    | Add MIT licence                                               | yesterday    |
| README.md  | DevOps Release Agent: record published links [skip ci]        | 10 hours ago |

README MIT license

## Equipment Calibration Compliance

Generated by the Agentic SDLC workflow.

Generated by the Agentic SDLC / Software Factory. Every change reaches this repository through an approved human gate — no agent merges its own work.

About

Calibration due dates are tracked on a spreadsheet held by one metrology technician, so instruments drift past due without anyone noticing until an auditor asks. As-found readings are written on a certificate pad and filed, which means that when an instrument is found out of tolerance nobody can answer the only question that matters: which product

ReadmeMIT licenseActivity0 stars0 watching0 forksReport repository

Releases

No releases published

Contributors 1

 csdmichael Michael Yaacoub

## README

The README explains architecture and folder layout and contains published UI, API, Swagger, OpenAPI, health, and collection links updated by the release workflow.

READMEMIT license

Generated by the Agentic SDLC workflow.  
Generated by the Agentic SDLC / Software Factory. Every change reaches this repository through an approved human gate — no agent merges its own work.

Table of contents

1. Overview

2. Architecture

3. API surface

4. Screens

5. Folder structure

6. Getting started

7. Build and test

8. Deployment

9. Published links

10. Requirements scope

11. Intake documents

12. Licence

Overview

| Item               | Value                                                                                                                                       |
|--------------------|---------------------------------------------------------------------------------------------------------------------------------------------|
| Project            | Equipment Calibration Compliance                                                                                                            |
| Business owner     | <a href="mailto:myaacoub@microsoft.com">myaacoub@microsoft.com</a>                                                                          |
| IT owner           | <a href="mailto:myaacoub@microsoft.com">myaacoub@microsoft.com</a>                                                                          |
| Target environment | Dev                                                                                                                                         |
| Work items         | Equipment Calibration Compliance                                                                                                            |
| Repository         | <a href="https://github.com/csdmichael/equipment-calibration-compliance">https://github.com/csdmichael/equipment-calibration-compliance</a> |

Releases

No releases published

Contributors 1

csdmichael

Michael Yaacoub

Languages

Python 47.1%

TypeScript 37.8%

JavaScript 10.9%

HTML 2.5%

SCSS 1.7%

## Pull request

Code is proposed on an agent branch and must pass the Pull Request Review gate. The release agent verifies the persisted generated PR before merge; it never selects an unrelated stale PR.

PlatformSolutionsResourcesOpen SourceEnterprisePricing

Search / Sign in Sign up

csdmichael / equipment-calibration-compliance Public

Notifications Fork 0 Star 0

<> Code Issues Pull requests Actions Projects Security and quality Insights

# Code Generation Agent output — Equipment Calibration Compliance #2

Merged csdmichael merged 37 commits into main from feature/agent/90e0dff5 10 hours ago

Conversation 0 Commits 37 Checks 5 Files changed 3 +4 -34 0000

csdmichael commented 16 hours ago Owner ...

Generated by the Agentic SDLC code generation agent for project 'Equipment Calibration Compliance' (artifact 90e0dff5-5481-46e6-9532-787d8cffb8eb).

Scaffolds ui/, api/, db/, and docs/ plus CI and Azure deployment workflows (37 files).

csdmichael added 30 commits 16 hours ago

Scaffold README.md

Scaffold .github/workflows/ci.yml

Scaffold .github/workflows/deploy-azure.yml

Scaffold .github/scripts/record\_published\_links.py

Scaffold .gitignore

Scaffold ui/package.json

Scaffold ui/angular.json

Scaffold ui/tsconfig.json

da1ec0e

1cd168a

f54156a

6ab6071

5a2af62

db69f9f

b5d0efd

5e38272

Reviews

No reviews

Assignees

No one assigned

Labels

None yet

Projects

None yet

Milestone

No milestone

Development

Successfully merging this pull request may close these issues.

None yet

1 participant

## GitHub Actions deployment

The generated workflow uses OIDC, builds/tests UI and API, deploys both App Services, performs bounded health/CRUD smoke tests, and writes published links back to README.

The screenshot shows a GitHub Actions workflow run for the repository `csdmichael/equipment-calibration-compliance`. The workflow is named `Equipment Calibration Compliance: generated application scaffold #7`. The run was triggered by a push to the `main` branch (commit `6e34680`) and has a status of **Success**. The total duration is **6m 49s**. The workflow file is `deploy-azure.yml`, which runs on push. The run details show a **deploy** step that completed successfully in 6m 44s. There is one warning annotation: `Node.js 20 is deprecated. The following actions target Node.js 20 but are being forced to run on Node.js 24: actions/checkout@v4, actions/setup-node@...`. The left sidebar shows the workflow summary, including a list of jobs (All jobs, deploy) and links to run details, usage, and workflow file.

## Published Azure applications

The following native screenshots use the healthy Field Service Work Orders deployment because it provides populated user workflows and a matching API collection.

### Published UI

The generated Angular/Ionic application exposes the domain workflow. The queue is loaded from the deployed API and contains seeded work orders.

| Field service Work Orders      |                              |                       |                         |
|--------------------------------|------------------------------|-----------------------|-------------------------|
| WORK ORDER QUEUE               | ASSET DETAIL AND DIAGNOSTICS | SERVICE LOG AND PARTS | COMPLETION AND SIGN-OFF |
| <hr/>                          |                              |                       |                         |
| Sample Work Order 1<br>WO-0001 |                              |                       | new                     |
| <hr/>                          |                              |                       |                         |
| Sample Work Order 2<br>WO-0002 |                              |                       | in-progress             |
| <hr/>                          |                              |                       |                         |
| Sample Work Order 3<br>WO-0003 |                              |                       | complete                |
| <hr/>                          |                              |                       |                         |
| Sample Work Order 4<br>WO-0004 |                              |                       | new                     |
| <hr/>                          |                              |                       |                         |

Selecting an item opens operational detail and enables the remaining service workflow tabs.

| Field service Work Orders  |                              |                       |                         |
|----------------------------|------------------------------|-----------------------|-------------------------|
| WORK ORDER QUEUE           | ASSET DETAIL AND DIAGNOSTICS | SERVICE LOG AND PARTS | COMPLETION AND SIGN-OFF |
| <hr/>                      |                              |                       |                         |
| <b>Sample Work Order 1</b> |                              |                       |                         |
| Reference: WO-0001         |                              |                       |                         |
| Status: new                |                              |                       |                         |
| Priority: low              |                              |                       |                         |
| <hr/>                      |                              |                       |                         |

## Published API

FastAPI Swagger documents health plus generated collection CRUD operations and schemas.

The screenshot displays the Swagger UI for the 'Field service Work Orders API'. At the top, the API title is followed by version '0.1.0' and 'OAS 3.1' in a green badge. Below this is the OpenAPI JSON file path and a description: 'REST API for Field service Work Orders. Generated by the Agentic SDLC workflow.' The interface is organized into expandable sections. The 'health' section, described as a 'Liveness probe used by the deploy pipeline.', contains a single GET endpoint at '/health' with the description 'Health'. The 'work-orders' section, described as 'Work Orders managed by this service.', lists five endpoints: a GET endpoint for listing items, a POST endpoint for creating items, and GET, PATCH, and DELETE endpoints for individual item management. Each endpoint is color-coded by method (blue for GET, green for POST/PATCH, red for DELETE). The 'Schemas' section at the bottom shows two error schemas: 'HTTPValidationError' and 'ValidationError', both of type 'object'.

**Field service Work Orders API** 0.1.0 OAS 3.1  
/openapi.json  
REST API for Field service Work Orders. Generated by the Agentic SDLC workflow.

**health** Liveness probe used by the deploy pipeline.

GET /health Health

**work-orders** Work Orders managed by this service.

GET /api/work-orders List Items

POST /api/work-orders Create Item

GET /api/work-orders/{item\_id} Get Item

PATCH /api/work-orders/{item\_id} Update Item

DELETE /api/work-orders/{item\_id} Delete Item

**Schemas**

HTTPValidationError > Expand all object

ValidationError > Expand all object

## App Service resources

The release evidence project has separate Linux UI and API App Services plus an App Service plan. The live ARM response confirms resource names, hostnames, region, state, kind, and SKU.

## Published Azure App Services

Generated UI, API, and hosting plan

Azure Resource Manager - resource group ai-myaacoub

Captured 2026-08-28 03:30 UTC

**2**

Published web apps

**F1**

Plan SKU

**West US 2**

Azure region

**Healthy**

Deployment state

### Generated Azure hosting resources

| Role             | Resource                              | State   | Hostname                                               | Location  | Kind / SKU |
|------------------|---------------------------------------|---------|--------------------------------------------------------|-----------|------------|
| UI App Service   | equipment-calibration-compliance-ui   | Running | equipment-calibration-compliance-ui.azurewebsites.net  | West US 2 | app,linux  |
| API App Service  | equipment-calibration-compliance-api  | Running | equipment-calibration-compliance-api.azurewebsites.net | West US 2 | app,linux  |
| App Service plan | equipment-calibration-compliance-plan | Active  | —                                                      | West US 2 | F1         |

Evidence generated from live Azure DevOps or Azure Resource Manager APIs because interactive portal sign-in is not available to the unattended documentation browser.

## Administration

### User Management

App Owners create or update users, role, identity provider, disabled state, and optional GitHub username. The directory shows authentication method and status. App Owner safeguards prevent removal or demotion of the last active owner.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

User Management

App Owner only. Add or edit users and set each user's authentication method.

Add or edit user

Saving an existing email updates that user in place.

Name

Jane Doe

Email

name@company.com

Role

Business User

Authentication method

Entra ID

Save user

Directory

5 user(s)

| USER                                                                             | ROLE                 | AUTHENTICATION      | ACTIONS                           |
|----------------------------------------------------------------------------------|----------------------|---------------------|-----------------------------------|
| <div>Vinay Gandhi</div> <div>admin@mngenvmcap662747.onmicrosoft.com</div>        | <div>Admin</div>     | <div>OTP</div>      | <div>Edit</div> <div>Remove</div> |
| <div>Admin (Demo Tenant)</div> <div>admin@mngenvmcap829495.onmicrosoft.com</div> | <div>App Owner</div> | <div>Entra ID</div> | <div>Edit</div> <div>Remove</div> |
| <div>Michael Yaacoub</div> <div>myaacoub@microsoft.com</div>                     | <div>App Owner</div> | <div>OTP</div>      | <div>Edit</div> <div>Remove</div> |

## Project Access - grant

Project Access accepts pasted Outlook-style contacts or manual rows, selects one or more projects, and grants ADO Contributors, optional GitHub collaborator, and Factory administrator access. Leaving GitHub username blank intentionally skips GitHub while continuing ADO and Factory access.



Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

**Project Access**

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Project Access

Grant or remove access for the same people across one or more existing projects.

Paste contacts

Paste names and emails separated by commas, semicolons, or new lines.

Contact list

Jane Doe <jane.doe@contoso.com>; John Smith <john.smith@contoso.com>

Extract contacts

Recipients

Each email is managed in ADO Contributors and SDLC Admins. GitHub access is optional.

Name

Jane Doe

Email

name@company.com

GitHub username (optional)

octocat

Add recipient

Projects

Choose every project these recipients should be able to access.

Existing projects

Select projects

0 selected

## Project Access - remove

Remove mode reverses access recorded by this workflow. It removes only managed ADO/GitHub memberships, preserves access that existed before the grant, and restores the prior Factory role when the last managed project is removed. Durable progress events and audit records show each decision.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Contact list

Jane Doe <jane.doe@contoso.com>; John Smith <john.smith@contoso.com>

Extract contacts

Recipients

Each email is managed in ADO Contributors and SDLC Admins. GitHub access is optional.

Name

Jane Doe

Email

name@company.com

GitHub username (optional)

octocat

+ Add recipient

Projects

Choose every project these recipients should be able to access.

Existing projects

Select projects

0 selected

GRANT

REMOVE

Remove access

## Role Permissions

Role Permissions displays the effective capability matrix, immutable App Owner protection, and locked capabilities. Changes are validated server-side and can be reset to configuration defaults.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Role Permissions

What each application role may do in the agentic workflow. App Owner and Admin can change this; every capability is re-checked server-side on each API call.

Restore defaults

Save

Permission matrix

Using the shipped defaults, App Owner holds every capability and cannot be reduced.

| CAPABILITY                                                                                                  | BUSINESS USER                       | IT USER                             | ADMIN                               | APP OWNER                           |
|-------------------------------------------------------------------------------------------------------------|-------------------------------------|-------------------------------------|-------------------------------------|-------------------------------------|
| Projects                                                                                                    |                                     |                                     |                                     |                                     |
| <b>View projects</b><br>See projects, workflow runs, artifacts, and agent output.                           | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> |
| <b>Create projects</b><br>Run the New Project wizard and submit for Plan & Scope approval.                  | <input checked="" type="checkbox"/> | <input type="checkbox"/>            | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> |
| <b>Manage projects</b><br>Archive or delete projects and override project-level systems of record.          | <input type="checkbox"/>            | <input type="checkbox"/>            | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> |
| Approvals                                                                                                   |                                     |                                     |                                     |                                     |
| <b>Approve business gates</b><br>Decide Plan & Scope, Backlog, and Test Acceptance gates.                   | <input checked="" type="checkbox"/> | <input type="checkbox"/>            | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> |
| <b>Approve technical gates</b><br>Decide Architecture, Code Generation, Pull Request, and Deployment gates. | <input type="checkbox"/>            | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> |
| <b>Approve any gate</b><br>Decide any gate regardless of its required role.                                 | <input type="checkbox"/>            | <input type="checkbox"/>            | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> |
| Agents                                                                                                      |                                     |                                     |                                     |                                     |
| <b>View agents</b><br>See agent definitions, models, routes, and run history.                               | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> |
| <b>Configure agents</b>                                                                                     | <input type="checkbox"/>            | <input type="checkbox"/>            | <input checked="" type="checkbox"/> | <input checked="" type="checkbox"/> |

## Agent Configuration

Agent Configuration controls enabled state, model, temperature, input/output limits, tools, MCP servers, approval behavior, and guardrails for the 12 configured roles. Foundry base identities use ordered 010- through 120- names.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Agent Configuration

Every agent's model, APIM route, guardrails, and approval requirement are data-driven. Expand an agent to edit it.

|                               |                                                                                                                    |                      |         |   |
|-------------------------------|--------------------------------------------------------------------------------------------------------------------|----------------------|---------|---|
| Requirements Agent            | Plan · model-router · foundry-agents(projectPath)/agents/{foundryAgentName}/endpoint/protocols/openai/responses    | Gated: business_user | Enabled | ▼ |
| Planning Agent                | Plan · model-router · foundry-agents(projectPath)/agents/{foundryAgentName}/endpoint/protocols/openai/responses    | Gated: business_user | Enabled | ▼ |
| Architecture Advisor Agent    | Design · gpt-5.4 · foundry-agents(projectPath)/agents/{foundryAgentName}/endpoint/protocols/openai/responses       | Gated: it_user       | Enabled | ▼ |
| Code Generation Agent         | Build · gpt-5.1-codex · foundry-agents(projectPath)/agents/{foundryAgentName}/endpoint/protocols/openai/responses  | Gated: it_user       | Enabled | ▼ |
| Test Planning Agent           | Test · model-router · foundry-agents(projectPath)/agents/{foundryAgentName}/endpoint/protocols/openai/responses    | Gated: it_user       | Enabled | ▼ |
| Testing Agent                 | Test · gpt-5.1-codex · foundry-agents(projectPath)/agents/{foundryAgentName}/endpoint/protocols/openai/responses   | Gated: admin         | Enabled | ▼ |
| Test Automation Agent         | Test · gpt-5.1-codex · foundry-agents(projectPath)/agents/{foundryAgentName}/endpoint/protocols/openai/responses   | Gated: admin         | Enabled | ▼ |
| Security and Compliance Agent | Security · gpt-5.4 · foundry-agents(projectPath)/agents/{foundryAgentName}/endpoint/protocols/openai/responses     | Gated: admin         | Enabled | ▼ |
| DevOps / Release Agent        | Deploy · gpt-5.4 · foundry-agents(projectPath)/agents/{foundryAgentName}/endpoint/protocols/openai/responses       | Gated: it_user       | Enabled | ▼ |
| Ops Monitoring Agent          | Operate · model-router · foundry-agents(projectPath)/agents/{foundryAgentName}/endpoint/protocols/openai/responses | Gated: it_user       | Enabled | ▼ |
| Knowledge Assistant           | Operate · model-router · foundry-agents(projectPath)/agents/{foundryAgentName}/endpoint/protocols/openai/responses |                      | Enabled | ▼ |
| Insights Agent                |                                                                                                                    |                      |         | ▼ |

## Global Settings

Global Settings manages model policy and system-of-record defaults inherited by projects. Only agent-compatible live Foundry deployments appear in model dropdowns.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Global Settings

Model and System of Record defaults apply to every project unless a project overrides them. Changes are audited.

Agent model defaults

Discovered from the configured Microsoft Foundry account. Model Router uses **balanced** routing to balance cost and quality for mixed-complexity work.

|                               |                                         |
|-------------------------------|-----------------------------------------|
| Requirements Agent            | model-router (balanced: cost + quality) |
| Planning Agent                | model-router (balanced: cost + quality) |
| Architecture Advisor Agent    | gpt-5.4                                 |
| Code Generation Agent         | gpt-5.1-codex                           |
| Test Planning Agent           | model-router (balanced: cost + quality) |
| Testing Agent                 | gpt-5.1-codex                           |
| Test Automation Agent         | gpt-5.1-codex                           |
| DevOps / Release Agent        | gpt-5.4                                 |
| Security and Compliance Agent | gpt-5.4                                 |
| Ops Monitoring Agent          | model-router (balanced: cost + quality) |
| Knowledge Assistant           | model-router (balanced: cost + quality) |
| Insights Agent                | model-router (balanced: cost + quality) |

Save model defaults

Reset to recommendations

Documentation

## APIM and Configuration

APIM & Configuration presents sanitized runtime configuration and connector readiness without exposing secrets. All model execution remains behind the configured APIM gateway.

Agentic SDLC — Software Factory

MYMichael YaacoubApp OwnerSign out

Agentic SDLCSoftware Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

APIM & Configuration

Read-only view of non-secret configuration. Secrets are never returned by the API — values come from each tier's config folder.

System of record connectors

Live connectivity probe. Mock mode never calls the external API.

| CONNECTOR    | MODE | STATUS    | DETAIL                                                                                          |
|--------------|------|-----------|-------------------------------------------------------------------------------------------------|
| GitHub       | live | connected | { "login": "csdmichael", "name": "Michael Yaacoub", "accountType": "User" }                     |
| Azure DevOps | live | connected | { "organizationUrl": "https://dev.azure.com/csdmichael", "projectCount": 9, "authMode": "pat" } |

APIM gateway

```
{  "$comment": "APIM gateway configuration in front of Azure AI Foundry. All Foundry calls route through APIM. Subscription key / MSI come from env, never here.",  "gateway": {    "baseUrl": "https://ai-gateway-apim-pec-my.azure-api.net",    "authMode": "subscription-key",    "subscriptionKeyHeader": "Ocp-Apim-Subscription-Key",    "correlationIdHeader": "x-correlation-id",    "timeoutMs": 300000,    "retry": {      "maxRetries": 2,      "backoffMs": 500,      "retryOnStatuses": [        429,        500,        502,        503,        504      ]    }  },  "workflowRetry": {    "maxRetries": 3,    "backoffSeconds": 15,  }}
```

# In-app documentation

The application includes role-accessible reference topics.

## Overview

Overview summarizes the governed factory and consolidated architecture.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Overview

A governed software factory where 12 named Microsoft Foundry Prompt Agents produce reviewable SDLC proposals under configurable human and automated approval policies.

Microsoft Agent Framework owns sequential workflow topology and pause/resume behavior. Azure API Management is the only model execution boundary.

Agent output is saved first. Review modes let humans edit and select artifacts; autonomous mode validates evidence and records system decisions before publication.

Microsoft

Agentic SDLC Software Factory — Enterprise Architecture

Diagram 1 of 2

People & Experiences

Business Stakeholders

Product Owners

Developers

QA / Testers

DevOps / Platform Engineers

Operations

Agentic SDLC Factory (Azure)

1 Sign in & submit project

FastAPI (Python)

Azure App Service

Authentication & RBAC

Project provisioning

Approval gates

Audit

Connector governance

2 Orchestrate workflow

Microsoft Agent Framework

Orchestration

Ordered workflow

Pause / resume

Shared context

Checkpoints

3 Invoke agents

API Management

Azure API Management

AI Gateway

Policy enforcement

Managed identity

Throttling

Correlation

Model routing

4 review & approve

Approval Workspace

Human checkpoint

5 Cosmos DB SQL API

Workflow state, artifacts, approvals, checkpoints, audit

6 Application Insights

Traces, model calls, dependencies

7 Observe & improve

FastAPI Connector Layer

Governed REST APIs & MCP allow-list

API

Systems of Record

Azure DevOps

Projects

Work items

Test plans

Pipelines

Wiki

GitHub

Repos

Branches

Pull requests

Workflows / actions

Source / docs

7 Deploy

ADO Test Plans

OIDC, no client secret

Azure Runtime

Azure Resource Manager

App Service / APIs

Managed Identity

Published Applications

Monitoring

Foundation

Microsoft Entra ID

users, app roles, managed identities, 12 agent identities, GitHub OIDC


Security & Governance

least-privilege RBAC, Key Vault, private connectivity, policy, audit, correlation IDs

Agent output is proposal-first; external writes follow the selected approval policy.

## Architecture

Architecture explains UI, API, persistence, Agent Framework, APIM, Foundry, and external systems.

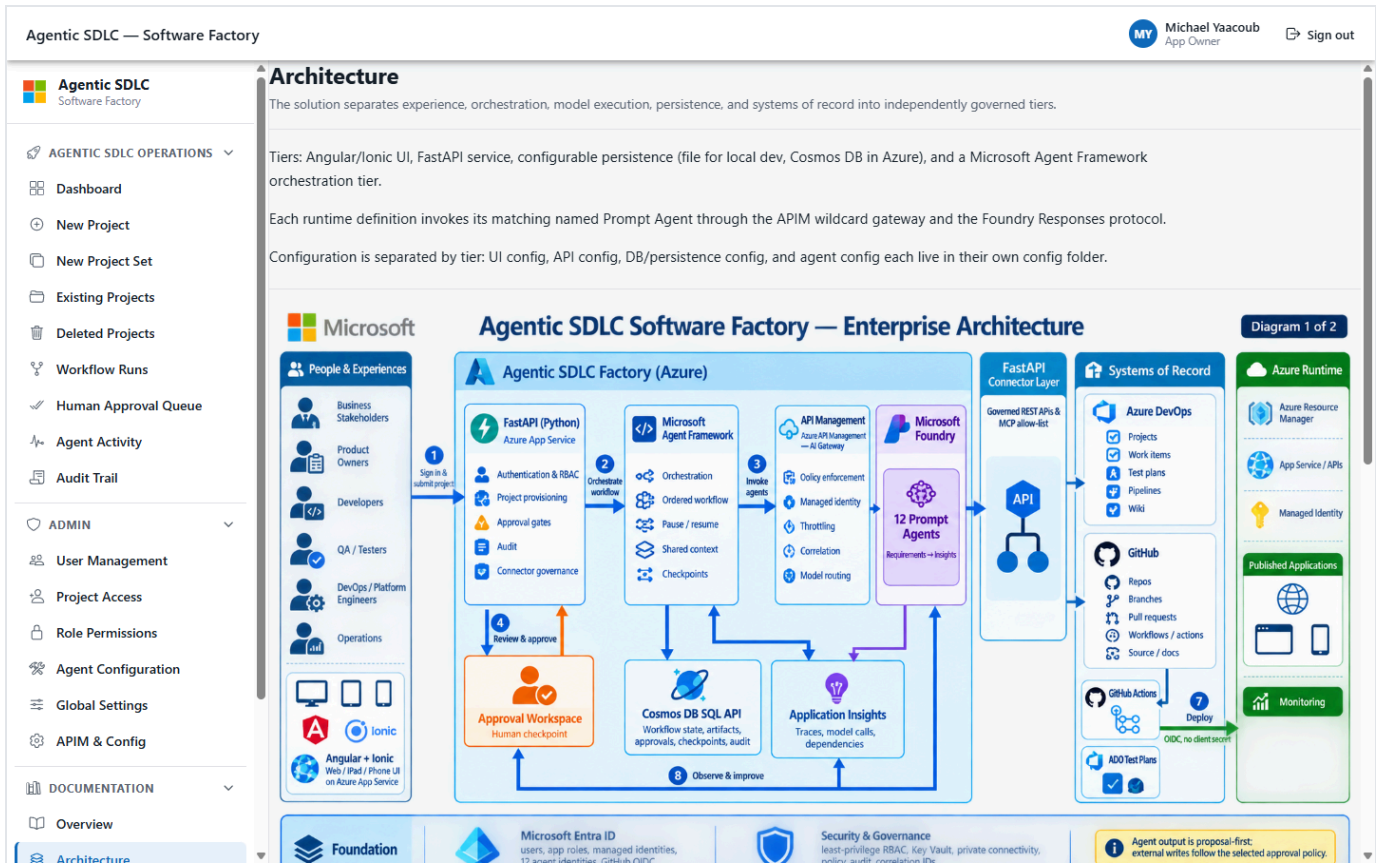

## Human-in-the-loop

This topic explains all nine gates and policy-dependent accountability.



Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Human-in-the-loop model

Nine explicit gates separate generation from publication. Project policy decides which gates require human action.

Nine approval gates span the lifecycle: Plan & Scope, Architecture & Design, Backlog Generation, Code Generation, Pull Request, Security Review, Test Acceptance, Release & Deployment, and Operate & Improve.

Human review pauses at every gate, minimal intervention pauses at four consequential checkpoints, and fully autonomous execution validates evidence and records system decisions without a user click.

The API validates role, prerequisite gate, artifact ownership, artifact review state, and selected references before publication. UI checks are ergonomic; the API is authoritative.

Every approve, reject, request-changes, and delegate decision records approver, role, timestamp, comments, previous/next state, delegation target, and artifact references.

## Agent responsibilities

Agent Responsibilities describes all 12 roles, stages, human owners, checkpoints, and outputs.

Agentic SDLC — Software Factory

MY

Michael Yaacoub

App Owner

Sign out

Agentic SDLC

Software Factory

AGENTIC SDLC OPERATIONS

Dashboard

New Project

New Project Set

Existing Projects

Deleted Projects

Workflow Runs

Human Approval Queue

Agent Activity

Audit Trail

ADMIN

User Management

Project Access

Role Permissions

Agent Configuration

Global Settings

APIM & Config

DOCUMENTATION

Overview

Architecture

Agent responsibilities

All 12 configured entries map one-to-one to named Prompt Agents in the Agentic SDLC Foundry project.

The UI shows each agent, its named Foundry identity, prerequisite, output gate, status, last run, and the human role or automated policy accountable for publication.

Logical phase diagrams are shared where several specialized agents collaborate in the same lifecycle stage.

1

Requirements Agent

Plan · Plan & Scope → Backlog Generation

1

Requirements Agent

(Plan & Scope)

INPUTS

Systems of Record

SharePoint documentation, business goals

Previous Agent

Business stakeholders

OUTPUTS

Systems of Record

Azure DevOps work items

Next Agent

Planning Agent

Analyzes requirements and creates traceable epics, features, user stories and acceptance criteria.

HUMAN OWNER

Business User / Product Owner

RESPONSIBILITY

Reads intake documents, identifies requirements, acceptance criteria, assumptions, and risks.

2

Planning Agent

Plan · Backlog Generation

2

Planning Agent

(Plan & Scope)

INPUTS

OUTPUTS

HUMAN OWNER


Business User / Product Owner

RESPONSIBILITY

Creates the editable Epic, Feature, User Story, Task, and sub-tasks selected

## Security and guardrails

Security & Guardrails explains identity, least privilege, secret handling, pre/post model checks, correlation, and audit.

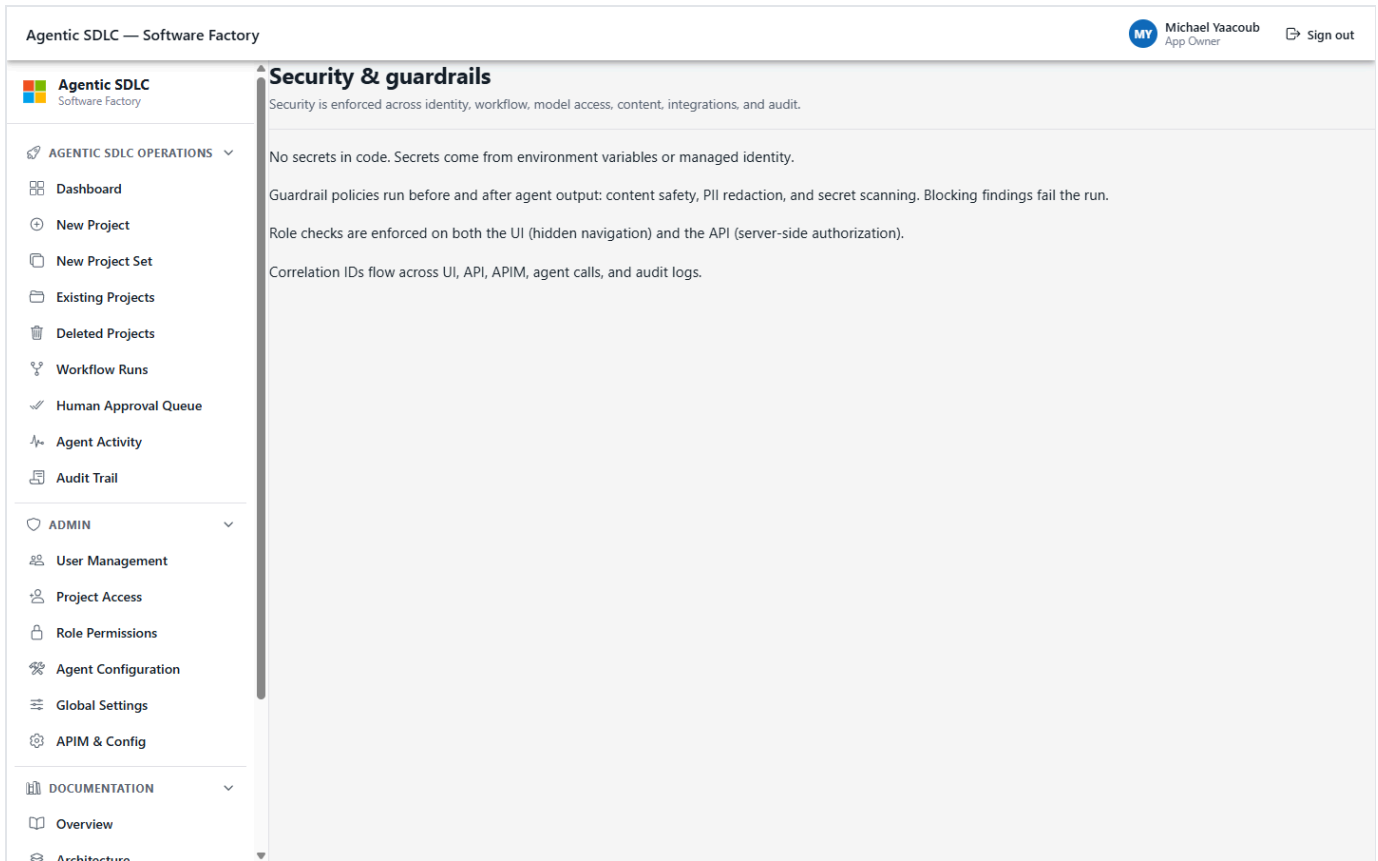

## End-to-end operating flow

1. An authorized creator opens New Project or New Project Set.
2. The creator supplies scope, owners, policy, and requirements, using defaults or Custom overrides.
3. The API validates input, provisions ADO/GitHub, publishes intake files, creates the durable workflow run, and sends owner notification.
4. Requirements and Planning agents produce scope and backlog proposals.
5. Policy or a human gate publishes reviewed work items, sprints, queries, dashboards, and delivery plan to ADO.
6. Architecture produces solution, data, API, security, and implementation decisions and publishes approved documentation.
7. Code Generation creates the complete GitHub repository on an agent branch and opens a pull request.
8. Test Planning, Testing, and Test Automation create ADO test assets and verify exact-commit CI evidence.
9. Security and Compliance validates findings and residual risk before release.
10. DevOps / Release configures GitHub OIDC, provisions Azure App Services, verifies/merges the persisted PR, dispatches one deployment, runs smoke tests, updates README links, closes related work items, and publishes the ADO wiki.
11. Ops Monitoring, Knowledge Assistant, and Insights produce operating and improvement evidence.
12. The run completes, audit remains queryable, owners receive completion notification, and a later revision can restart from an earlier stage.

# Screen index

| Screen                     | Route                 | Guide section                         |
|----------------------------|-----------------------|---------------------------------------|
| Sign in / request access   | /login                | Sign in                               |
| Dashboard                  | /dashboard            | Dashboard                             |
| New Project                | /projects/new         | Create a project                      |
| New Project Set            | /projects/new-set     | Create a project set                  |
| Existing Projects          | /projects             | Project directories                   |
| Deleted Projects           | /projects/deleted     | Project directories                   |
| Project Details            | /projects/:id         | Workflow policies and Project Details |
| Workflow Runs              | /workflow-runs        | Operational screens                   |
| Human Approval Queue       | /approvals            | Operational screens                   |
| Agent Activity             | /agent-activity       | Operational screens                   |
| Audit Trail                | /audit                | Operational screens                   |
| User Management            | /admin/users          | Administration                        |
| Project Access             | /admin/project-access | Administration                        |
| Role Permissions           | /admin/permissions    | Administration                        |
| Agent Configuration        | /admin/agents         | Administration                        |
| Global Settings            | /admin/settings       | Administration                        |
| APIM & Configuration       | /admin/config         | Administration                        |
| Overview documentation     | /docs/overview        | In-app documentation                  |
| Architecture documentation | /docs/architecture    | In-app documentation                  |
| HITL documentation         | /docs/hitl            | In-app documentation                  |
| Agent Responsibilities     | /docs/agents          | In-app documentation                  |
| Security & Guardrails      | /docs/security        | In-app documentation                  |

## Troubleshooting

- **A project is waiting:** Open Project Details and inspect the first Awaiting Approval gate, missing evidence message, or failed automation banner.
- **An agent cannot run:** Confirm its prerequisite gate, selected-agent policy, model availability, APIM path, and circuit-breaker state.
- **ADO or GitHub publication failed:** Open Generated Assets, Agent Runs & Artifacts, and Audit Trail for the exact connector error and correlation ID.

- **A project has no description:** New intake derives two or three sentences from readable functional requirements when the description is blank.
- **GitHub access should be skipped:** Leave GitHub username blank in Project Access. Do not enter a placeholder value.
- **Access must be removed:** Use Project Access Remove mode with the same email and selected projects. Pre-existing memberships are preserved.
- **A generated API is cold:** Warm `/health` , then reload the UI. App Service startup may take longer on a shared free/basic plan.
- **A deployment appears stale:** Verify the exact GitHub Actions run and deployed behavior; App Service may need a worker recycle after some deployment methods.
- **Native ADO capture prompts for credentials:** Use approved interactive organizational sign-in. This guide uses live REST-backed evidence panels rather than storing browser credentials.

## Production references

---

- Factory UI: <https://agentic-sdlc-ui-my.azurewebsites.net>
- Factory API: <https://agentic-sdlc-api-my.azurewebsites.net>
- Application repository: <https://github.com/csdmichael/Foundry-Agentic-Workflow-SDLC>
- Documentation repository: <https://github.com/csdmichael/Foundry-Agentic-Workflow-SDLC-Docs>
- Generated Equipment Calibration repository: <https://github.com/csdmichael/equipment-calibration-compliance>
- Published Field Service UI: <https://field-service-work-orders-ui.azurewebsites.net>
- Published Field Service Swagger: <https://field-service-work-orders-api.azurewebsites.net/docs>
